


Sequoyah 2

1Q/2013 Performance Indicators

Licensee's General Comments: none

Unplanned Scrams per 7000 Critical Hrs

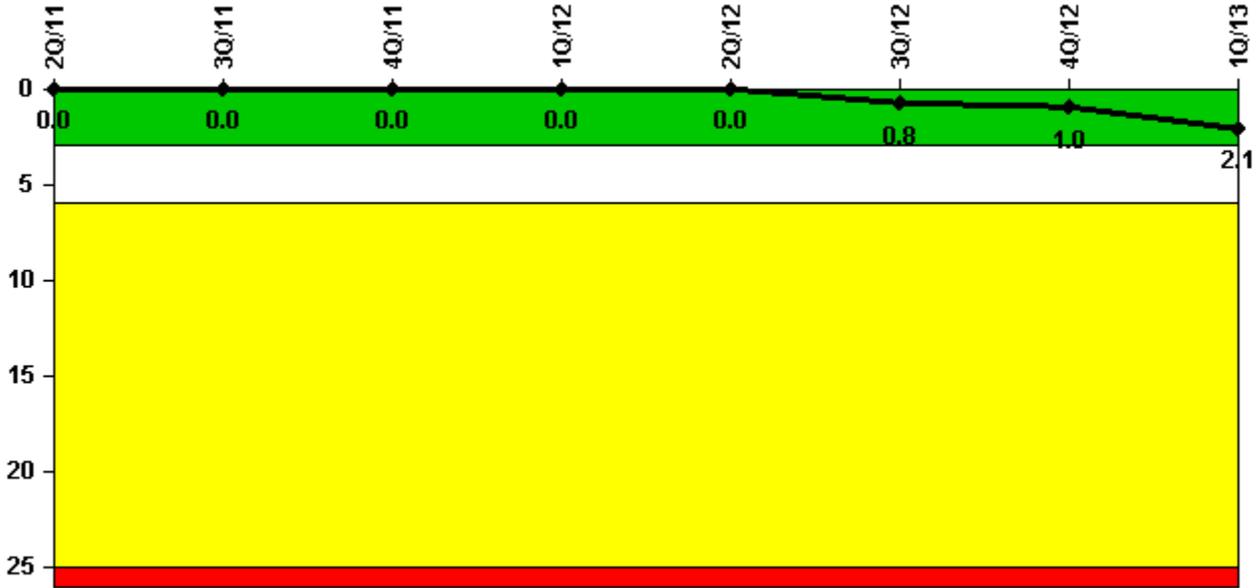


Thresholds: White > 3.0 Yellow > 6.0 Red > 25.0

Notes

Unplanned Scrams per 7000 Critical Hrs	2Q/11	3Q/11	4Q/11	1Q/12	2Q/12	3Q/12	4Q/12	1Q/13
Unplanned scrams	0	0	0	0	0	1.0	0	1.0
Critical hours	1459.1	2208.0	2209.0	2183.0	2184.0	2167.9	336.0	2055.3
Indicator value	0	0	0	0	0	0.8	1.0	2.1

Licensee Comments: none

Unplanned Power Changes per 7000 Critical Hrs

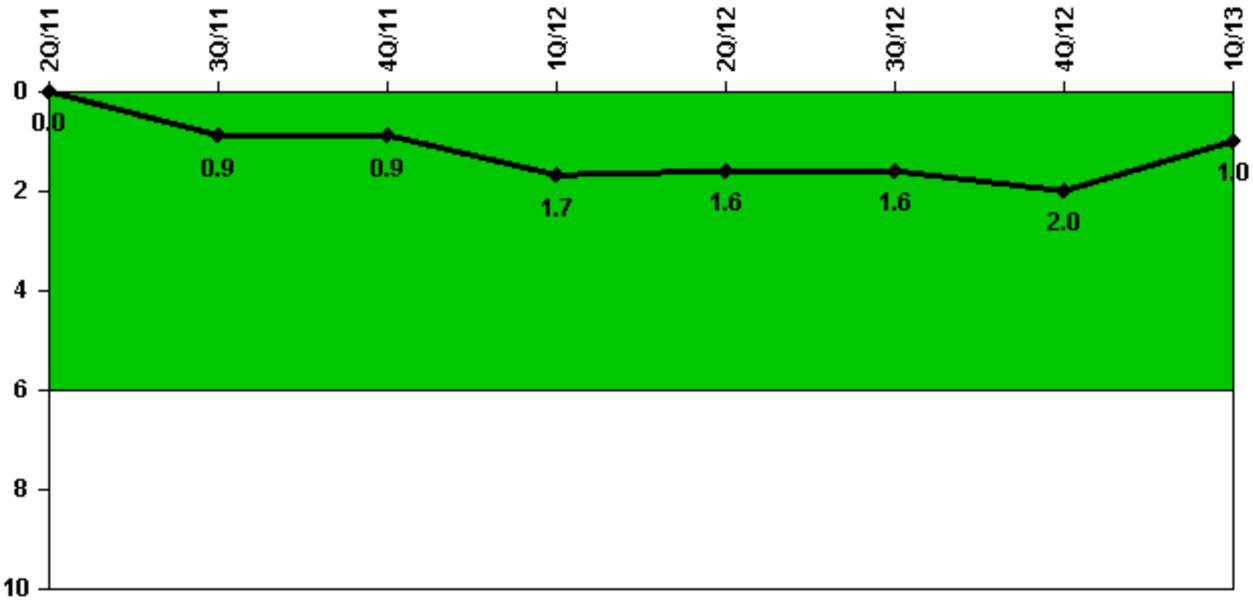


Thresholds: White > 6.0

Notes

Unplanned Power Changes per 7000 Critical Hrs	2Q/11	3Q/11	4Q/11	1Q/12	2Q/12	3Q/12	4Q/12	1Q/13
Unplanned power changes	0	1.0	0	1.0	0	1.0	0	0
Critical hours	1459.1	2208.0	2209.0	2183.0	2184.0	2167.9	336.0	2055.3
Indicator value	0	0.9	0.9	1.7	1.6	1.6	2.0	1.0

Licensee Comments: none

Unplanned Scrams with Complications

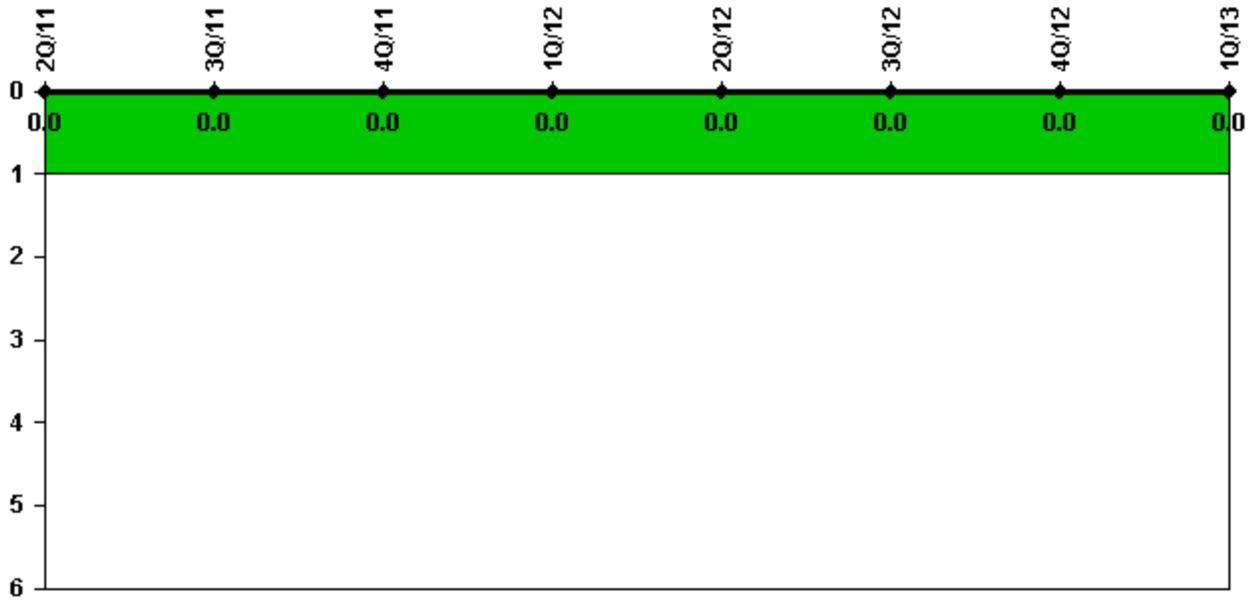


Thresholds: White > 1.0

Notes

Unplanned Scrams with Complications	2Q/11	3Q/11	4Q/11	1Q/12	2Q/12	3Q/12	4Q/12	1Q/13
Scrams with complications	0	0	0	0	0	0	0	0
Indicator value	0.0							

Licensee Comments: none

Safety System Functional Failures (PWR)

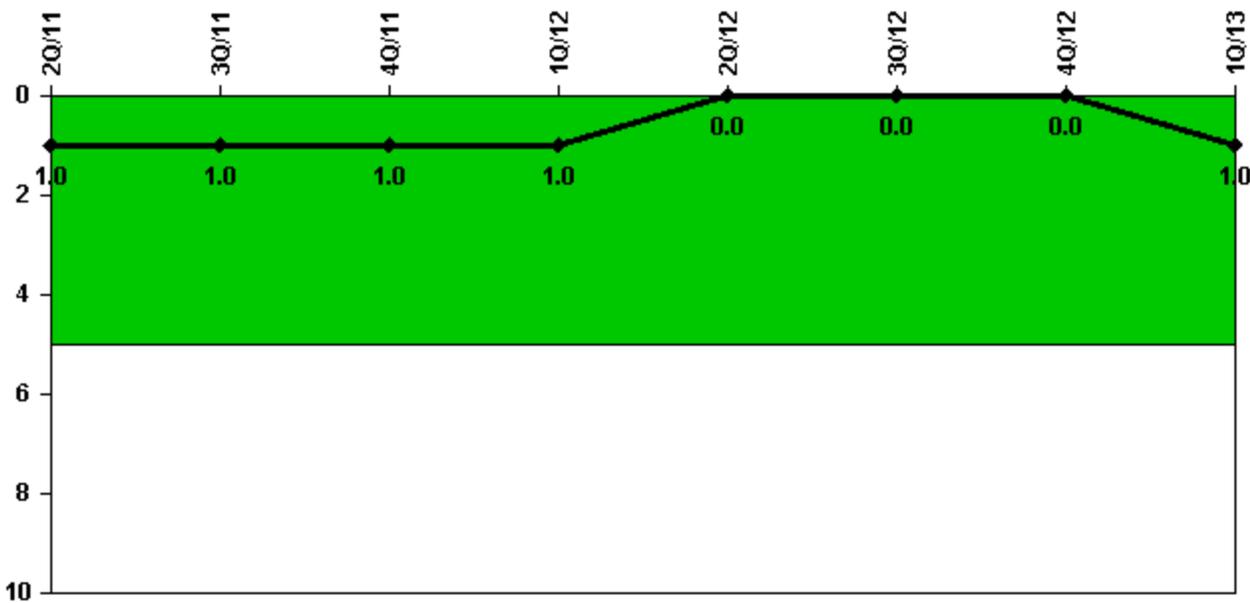

Thresholds: White > 5.0

Notes


Safety System Functional Failures (PWR)	2Q/11	3Q/11	4Q/11	1Q/12	2Q/12	3Q/12	4Q/12	1Q/13
Safety System Functional Failures	1	0	0	0	0	0	0	1
Indicator value	1	1	1	1	0	0	0	1

Licensee Comments:

4Q/12: The PRA Model of Record was revised 9/1/2012, updating the PRA model using the CAFTA program. The base numbers used in the MSPI database were also updated in accordance with NEI 99-02 Rev 6. As a result of the PRA model change, the CDF, Fussel-Vesely and Basic Event Probabilities for all monitored trains and components were revised.

2Q/11: LER 327, 328/2011-001-00, Both trains of main control room air conditioning system being inoperable, was reported as a safety system functional failure on April 15, 2011.

Mitigating Systems Performance Index, Emergency AC Power System

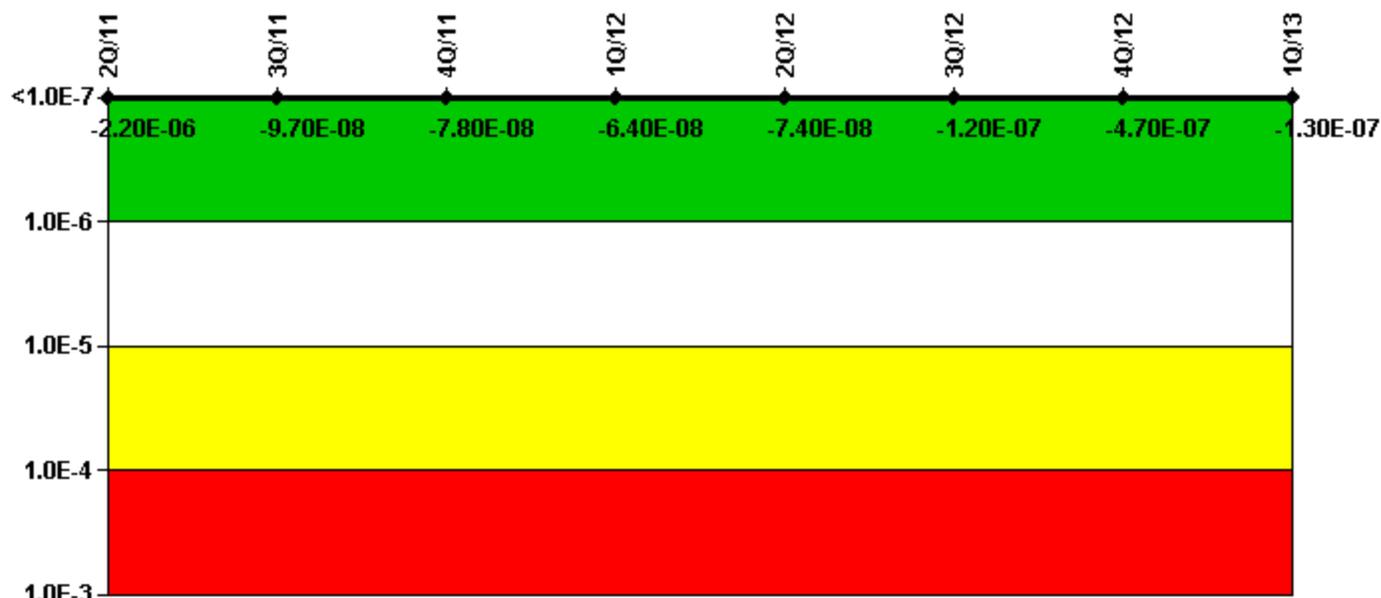

Thresholds: White > 1.00E-6 Yellow > 1.00E-5 Red > 1.00E-4

Notes

Mitigating Systems Performance Index, Emergency AC Power System	2Q/11	3Q/11	4Q/11	1Q/12	2Q/12	3Q/12	4Q/12	1Q/13
UAI (Δ CDF)	-2.74E-07	-8.25E-09	1.37E-08	2.48E-08	1.19E-08	1.09E-08	3.15E-08	5.43E-08
URI (Δ CDF)	-1.90E-06	-8.87E-08	-9.14E-08	-8.88E-08	-8.63E-08	-1.31E-07	-5.01E-07	-1.80E-07
PLE	NO							
Indicator value	-2.20E-06	-9.70E-08	-7.80E-08	-6.40E-08	-7.40E-08	-1.20E-07	-4.70E-07	-1.30E-07

Licensee Comments:

4Q/12: Changed PRA Parameter(s). The PRA Model of Record was revised 9/1/2012, updating the PRA model using the CAFTA program. The base numbers used in the MSPI database were also updated in accordance with NEI 99-02 Rev 6. As a result of the PRA model change, the CDF, Fussel-Vesely and Basic Event Probabilities for all monitored trains and components were revised.

1Q/12: Changed PRA Parameter(s). Revised PRA values and scoping for the PRA Model of Record dated 5/27/11 as recalculated in Calc MDN-000-999-2011-0255 Rev 1 & 2 including adding the EDG FO Pumps to scope as required by a FAQ to NEI 99-02. Errors in calc Rev 0 corrected in CDE back thru 3rd quarter 2011 as required by NEI 99-02. Ref PER 483857.


4Q/11: Changed PRA Parameter(s).

3Q/11: Changed PRA Parameter(s). The calculations to input into MSPI were performed using the current Sequoyah CAFTA PRA Model Rev 0. The PRA Model of Record was revised 5/27/11, updating the PRA model using

the CAFTA program. The base numbers used in the MSPI database were also updated in accordance with NEI 99-02 Rev 6. As a result of the PRA model change, the CDF, Fussel-Vesely and Basic Event Probabilities for all monitored trains and components were revised.

3Q/11: Changed PRA Parameter(s). The calculations to input into MSPI were performed using the current Sequoyah CAFTA PRA Model Rev 0. The PRA Model of Record was revised 5/27/11, updating the PRA model using the CAFTA program. The base numbers used in the MSPI database were also updated in accordance with NEI 99-02 Rev 6. As a result of the PRA model change, the CDF, Fussel-Vesely and Basic Event Probabilities for all monitored trains and components were revised.

Mitigating Systems Performance Index, High Pressure Injection System

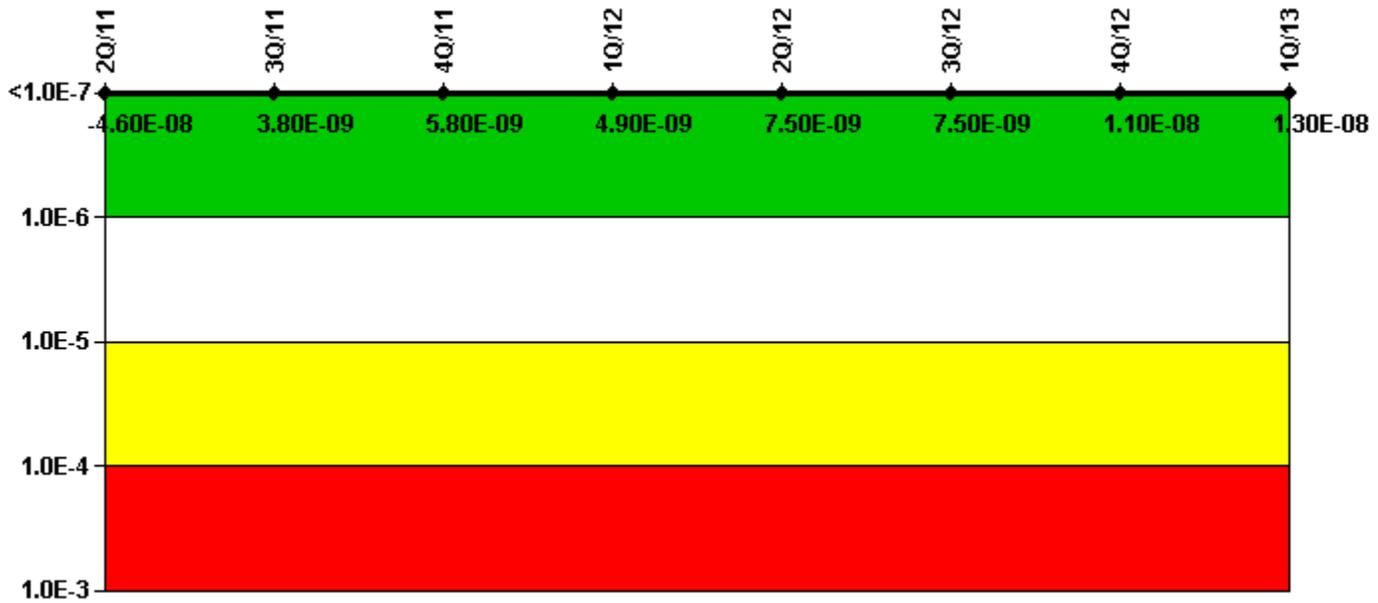

Thresholds: White > 1.00E-6 Yellow > 1.00E-5 Red > 1.00E-4

Notes

Mitigating Systems Performance Index, High Pressure Injection System	2Q/11	3Q/11	4Q/11	1Q/12	2Q/12	3Q/12	4Q/12	1Q/13
UAI (ΔCDF)	1.28E-07	4.23E-09	6.21E-09	5.37E-09	7.90E-09	7.92E-09	1.13E-08	1.33E-08
URI (ΔCDF)	-1.74E-07	-4.34E-10	-4.34E-10	-4.35E-10	-4.35E-10	-4.36E-10	-6.92E-10	-6.93E-10
PLE	NO							
Indicator value	-4.60E-08	3.80E-09	5.80E-09	4.90E-09	7.50E-09	7.50E-09	1.10E-08	1.30E-08

Licensee Comments:

4Q/12: Changed PRA Parameter(s). The PRA Model of Record was revised 9/1/2012, updating the PRA model using the CAFTA program. The base numbers used in the MSPI database were also updated in accordance with NEI 99-02 Rev 6. As a result of the PRA model change, the CDF, Fussel-Vesely and Basic Event Probabilities for all monitored trains and components were revised.

1Q/12: Revised PRA values and scoping for the PRA Model of Record dated 5/27/11 as recalculated in Calc MDN-000-999-2011-0255 Rev 1 & 2. Errors in calc Rev 0 corrected in CDE back thru 3rd quarter 2011 as required by NEI 99-02. Ref PER 483857.

1Q/12: Changed PRA Parameter(s). Revised PRA values and scoping for the PRA Model of Record dated 5/27/11 as recalculated in Calc MDN-000-999-2011-0255 Rev 1 & 2. Errors in calc Rev 0 corrected in CDE back thru 3rd quarter 2011 as required by NEI 99-02. Ref PER 483857.


4Q/11: Changed PRA Parameter(s).

3Q/11: Changed PRA Parameter(s). The calculations to input into MSPI were performed using the current Sequoyah CAFTA PRA Model Rev 0. The PRA Model of Record was revised 5/27/11, updating the PRA model using the CAFTA program. The base numbers used in the MSPI database were also updated in accordance with NEI 99-02 Rev 6. As a result of the PRA model change, the CDF, Fussel-Vesely and Basic Event Probabilities for all monitored trains and components were revised.

3Q/11: The calculations to input into MSPI were performed using the current Sequoyah CAFTA PRA Model Rev 0. The PRA Model of Record was revised 5/27/11, updating the PRA model using the CAFTA program. The base numbers used in the MSPI database were also updated in accordance with NEI 99-02 Rev 6. As a result of the PRA model change, the CDF, Fussel-Vesely and Basic Event Probabilities for all monitored trains and components were revised.

3Q/11: Changed PRA Parameter(s). The calculations to input into MSPI were performed using the current Sequoyah CAFTA PRA Model Rev 0. The PRA Model of Record was revised 5/27/11, updating the PRA model using the CAFTA program. The base numbers used in the MSPI database were also updated in accordance with NEI 99-02 Rev 6. As a result of the PRA model change, the CDF, Fussel-Vesely and Basic Event Probabilities for all monitored trains and components were revised.

Mitigating Systems Performance Index, Heat Removal System

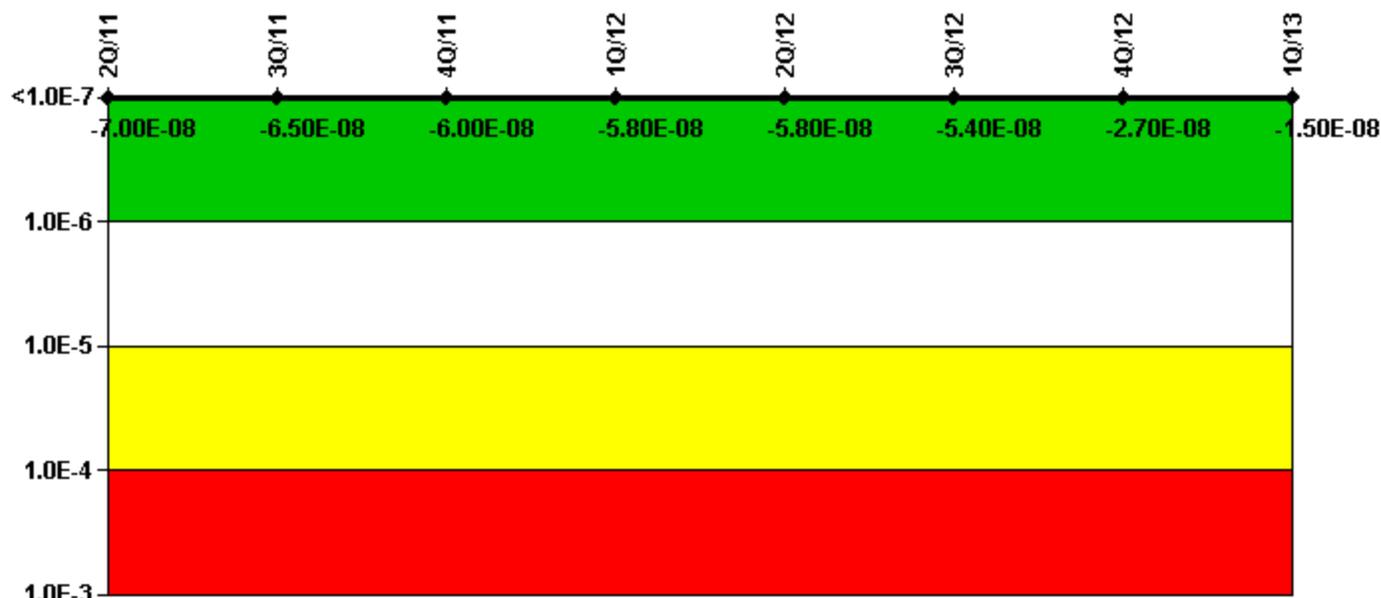

Thresholds: White > 1.00E-6 Yellow > 1.00E-5 Red > 1.00E-4

Notes

Mitigating Systems Performance Index, Heat Removal System	2Q/11	3Q/11	4Q/11	1Q/12	2Q/12	3Q/12	4Q/12	1Q/13
UAI (ΔCDF)	2.69E-08	2.10E-08	2.54E-08	2.52E-08	2.40E-08	2.94E-08	1.78E-08	3.08E-08
URI (ΔCDF)	-9.69E-08	-8.63E-08	-8.51E-08	-8.35E-08	-8.22E-08	-8.36E-08	-4.47E-08	-4.55E-08
PLE	NO							
Indicator value	-7.00E-08	-6.50E-08	-6.00E-08	-5.80E-08	-5.80E-08	-5.40E-08	-2.70E-08	-1.50E-08

Licensee Comments:

4Q/12: Changed PRA Parameter(s). The PRA Model of Record was revised 9/1/2012, updating the PRA model using the CAFTA program. The base numbers used in the MSPI database were also updated in accordance with NEI 99-02 Rev 6. As a result of the PRA model change, the CDF, Fussel-Vesely and Basic Event Probabilities for all monitored trains and components were revised.

1Q/12: Revised PRA values and scoping for the PRA Model of Record dated 5/27/11 as recalculated in Calc MDN-000-999-2011-0255 Rev 1 & 2. Errors in calc Rev 0 corrected in CDE back thru 3rd quarter 2011 as required by NEI 99-02. Ref PER 483857.


1Q/12: Revised PRA values and scoping for the PRA Model of Record dated 5/27/11 as recalculated in Calc MDN-000-999-2011-0255 Rev 1 & 2. Errors in calc Rev 0 corrected in CDE back thru 3rd quarter 2011 as required by NEI 99-02. Ref PER 483857.

3Q/11: The calculations to input into MSPI were performed using the current Sequoyah CAFTA PRA Model Rev 0. The PRA Model of Record was revised 5/27/11, updating the PRA model using the CAFTA program. The base numbers used in the MSPI database were also updated in accordance with NEI 99-02 Rev 6. As a result of the

PRA model change, the CDF, Fussel-Vesely and Basic Event Probabilities for all monitored trains and components were revised.

3Q/11: Changed PRA Parameter(s). The calculations to input into MSPI were performed using the current Sequoyah CAFTA PRA Model Rev 0. The PRA Model of Record was revised 5/27/11, updating the PRA model using the CAFTA program. The base numbers used in the MSPI database were also updated in accordance with NEI 99-02 Rev 6. As a result of the PRA model change, the CDF, Fussel-Vesely and Basic Event Probabilities for all monitored trains and components were revised.

Mitigating Systems Performance Index, Residual Heat Removal System

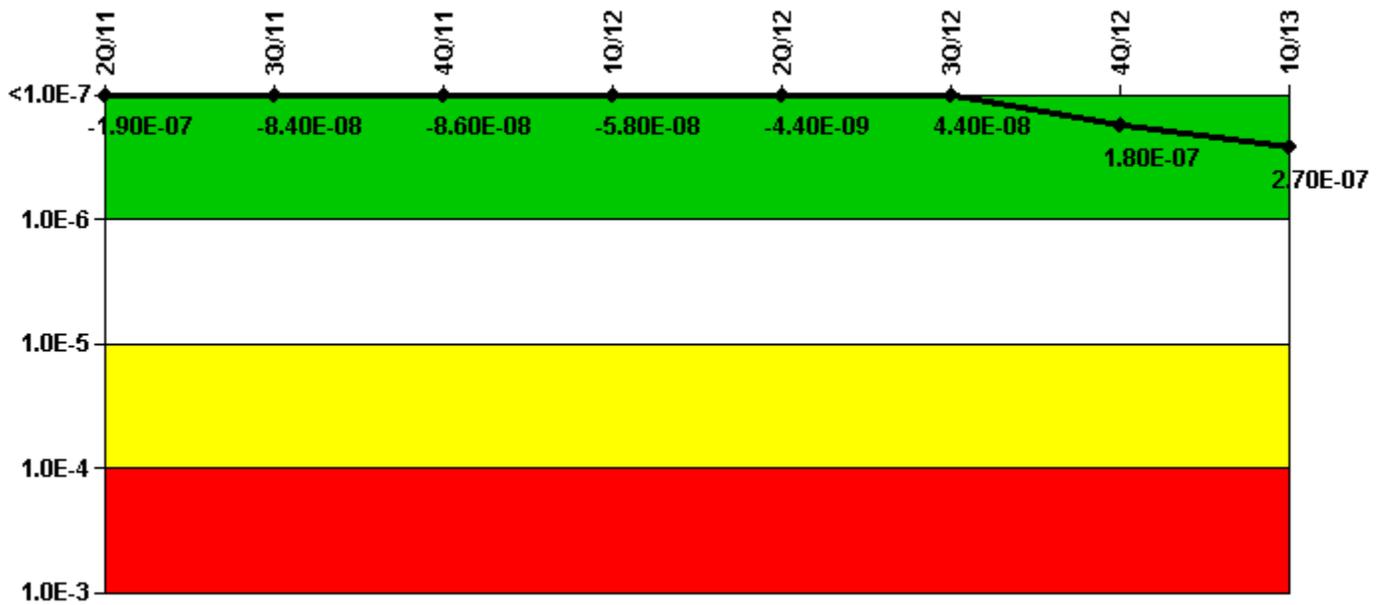

Thresholds: White > 1.00E-6 Yellow > 1.00E-5 Red > 1.00E-4

Notes

Mitigating Systems Performance Index, Residual Heat Removal System	2Q/11	3Q/11	4Q/11	1Q/12	2Q/12	3Q/12	4Q/12	1Q/13
UAI (ΔCDF)	1.70E-07	1.18E-07	1.16E-07	1.44E-07	1.98E-07	2.46E-07	4.47E-07	5.37E-07
URI (ΔCDF)	-3.62E-07	-2.02E-07	-2.02E-07	-2.02E-07	-2.02E-07	-2.02E-07	-2.64E-07	-2.66E-07
PLE	NO							
Indicator value	-1.90E-07	-8.40E-08	-8.60E-08	-5.80E-08	-4.40E-09	4.40E-08	1.80E-07	2.70E-07

Licensee Comments:

4Q/12: Changed PRA Parameter(s). The PRA Model of Record was revised 9/1/2012, updating the PRA model using the CAFTA program. The base numbers used in the MSPI database were also updated in accordance with NEI 99-02 Rev 6. As a result of the PRA model change, the CDF, Fussel-Vesely and Basic Event Probabilities for all monitored trains and components were revised.


1Q/12: Revised PRA values and scoping for the PRA Model of Record dated 5/27/11 as recalculated in Calc MDN-000-999-2011-0255 Rev 1 & 2. Errors in calc Rev 0 corrected in CDE back thru 3rd quarter 2011 as required by NEI 99-02. Ref PER 483857.

1Q/12: Revised PRA values and scoping for the PRA Model of Record dated 5/27/11 as recalculated in Calc MDN-000-999-2011-0255 Rev 1 & 2. Errors in calc Rev 0 corrected in CDE back thru 3rd quarter 2011 as required by NEI 99-02. Ref PER 483857.

3Q/11: The calculations to input into MSPI were performed using the current Sequoyah CAFTA PRA Model Rev 0. The PRA Model of Record was revised 5/27/11, updating the PRA model using the CAFTA program. The base numbers used in the MSPI database were also updated in accordance with NEI 99-02 Rev 6. As a result of the PRA model change, the CDF, Fussel-Vesely and Basic Event Probabilities for all monitored trains and components were revised.

3Q/11: Changed PRA Parameter(s). The calculations to input into MSPI were performed using the current Sequoyah CAFTA PRA Model Rev 0. The PRA Model of Record was revised 5/27/11, updating the PRA model using the CAFTA program. The base numbers used in the MSPI database were also updated in accordance with NEI 99-02 Rev 6. As a result of the PRA model change, the CDF, Fussel-Vesely and Basic Event Probabilities for all monitored trains and components were revised.

Mitigating Systems Performance Index, Cooling Water Systems

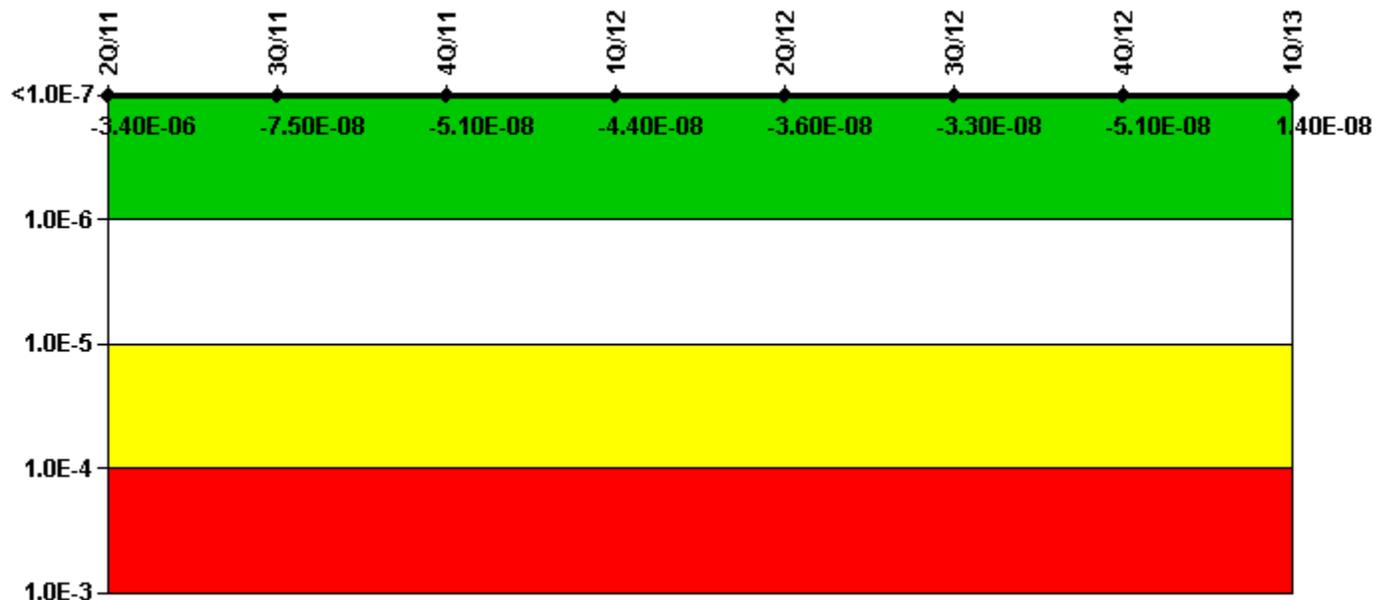

Thresholds: White > 1.00E-6 Yellow > 1.00E-5 Red > 1.00E-4

Notes

Mitigating Systems Performance Index, Cooling Water Systems	2Q/11	3Q/11	4Q/11	1Q/12	2Q/12	3Q/12	4Q/12	1Q/13
UAI (Δ CDF)	-3.17E-06	-1.77E-08	6.17E-09	1.28E-08	2.09E-08	2.40E-08	7.72E-08	1.43E-07
URI (Δ CDF)	-2.01E-07	-5.73E-08	-5.73E-08	-5.73E-08	-5.73E-08	-5.73E-08	-1.28E-07	-1.28E-07
PLE	NO	NO						
Indicator value	-3.40E-06	-7.50E-08	-5.10E-08	-4.40E-08	-3.60E-08	-3.30E-08	-5.10E-08	1.40E-08

Licensee Comments:

1Q/13: The planned unavailability baselines for all ERCW pumps were adjusted as needed to reflect past and current planned maintenance not performed every 3 years or less as specified by NEI 99-02.

4Q/12: Changed PRA Parameter(s). The PRA Model of Record was revised 9/1/2012, updating the PRA model using the CAFTA program. The base numbers used in the MSPI database were also updated in accordance with NEI 99-02 Rev 6. As a result of the PRA model change, the CDF, Fussel-Vesely and Basic Event Probabilities for all monitored trains and components were revised. The planned unavailability baselines for all ERCW pumps were adjusted as needed to reflect past and current planned maintenance not performed every 3 years or less as specified by NEI 99-02.

3Q/12: Changed PRA Parameter(s). The planned unavailability baselines for all ERCW pumps were adjusted as needed to reflect past and current planned maintenance not performed every 3 years or less as specified by NEI 99-02.

3Q/12: Changed PRA Parameter(s). The planned unavailability baselines for all ERCW pumps were adjusted as needed to reflect past and current planned maintenance not performed every 3 years or less as specified by NEI 99-02.

2Q/12: Changed PRA Parameter(s). The planned unavailability baselines for all ERCW pumps were adjusted as needed to reflect past and current planned maintenance not performed every 3 years or less as specified by NEI 99-02.

2Q/12: The planned unavailability baselines for all ERCW pumps were adjusted as needed to reflect past and current planned maintenance not performed every 3 years or less as specified by NEI 99-02.

1Q/12: Changed PRA Parameter(s). Revised PRA values and scoping for the PRA Model of Record dated 5/27/11 as recalculated in Calc MDN-000-999-2011-0255 Rev 1 & 2. Errors in calc Rev 0 corrected in CDE back thru 3rd quarter 2011 as required by NEI 99-02. Ref PER 483857. The planned unavailability baselines for all ERCW pumps were adjusted as needed to reflect past and current planned maintenance not performed every 3 years or less as specified by NEI 99-02.

1Q/12: Changed PRA Parameter(s). Revised PRA values and scoping for the PRA Model of Record dated 5/27/11 as recalculated in Calc MDN-000-999-2011-0255 Rev 1 & 2. Errors in calc Rev 0 corrected in CDE back thru 3rd quarter 2011 as required by NEI 99-02. Ref PER 483857. The planned unavailability baselines for all ERCW pumps were adjusted as needed to reflect past and current planned maintenance not performed every 3 years or less as specified by NEI 99-02.

4Q/11: Changed PRA Parameter(s). The planned unavailability baselines for all ERCW pumps were adjusted as needed to reflect past and current planned maintenance not performed every 3 years or less as specified by NEI 99-02.

4Q/11: The planned unavailability baselines for all ERCW pumps were adjusted as needed to reflect past and current planned maintenance not performed every 3 years or less as specified by NEI 99-02.

4Q/11: Changed PRA Parameter(s). The planned unavailability baselines for all ERCW pumps were adjusted as needed to reflect past and current planned maintenance not performed every 3 years or less as specified by NEI 99-02.

3Q/11: Changed PRA Parameter(s). The calculations to input into MSPI were performed using the current Sequoyah CAFTA PRA Model Rev 0. The PRA Model of Record was revised 5/27/11, updating the PRA model using the CAFTA program. The base numbers used in the MSPI database were also updated in accordance with NEI 99-02 Rev 6. As a result of the PRA model change, the CDF, Fussel-Vesely and Basic Event Probabilities for all monitored trains and components were revised. The planned unavailability baselines for all ERCW pumps were changed as needed to reflect past and current planned maintenance not performed every 3 years or less as specified by NEI 99-02.


3Q/11: Changed PRA Parameter(s). The calculations to input into MSPI were performed using the current Sequoyah CAFTA PRA Model Rev 0. The PRA Model of Record was revised 5/27/11, updating the PRA model using the CAFTA program. The base numbers used in the MSPI database were also updated in accordance with NEI 99-02 Rev 6. As a result of the PRA model change, the CDF, Fussel-Vesely and Basic Event Probabilities for all monitored trains and components were revised. The planned unavailability baselines for all ERCW pumps were changed as needed to reflect past and current planned maintenance not performed every 3 years or less as specified by NEI 99-02.

3Q/11: Changed PRA Parameter(s). The calculations to input into MSPI were performed using the current Sequoyah CAFTA PRA Model Rev 0. The PRA Model of Record was revised 5/27/11, updating the PRA model using the CAFTA program. The base numbers used in the MSPI database were also updated in accordance with NEI 99-02 Rev 6. As a result of the PRA model change, the CDF, Fussel-Vesely and Basic Event Probabilities for all monitored trains and components were revised. The planned unavailability baselines for all ERCW pumps were changed as needed to reflect past and current planned maintenance not performed every 3 years or less as specified by NEI 99-02.

2Q/11: Changed PRA Parameter(s). The planned unavailability baselines for all ERCW pumps were changed as needed to reflect past and current planned maintenance not performed every 3 years or less as specified by NEI 99-02.

2Q/11: Changed PRA Parameter(s). The planned unavailability baselines for all ERCW pumps were changed as needed to reflect past and current planned maintenance not performed every 3 years or less as specified by NEI 99-02.

Reactor Coolant System Activity

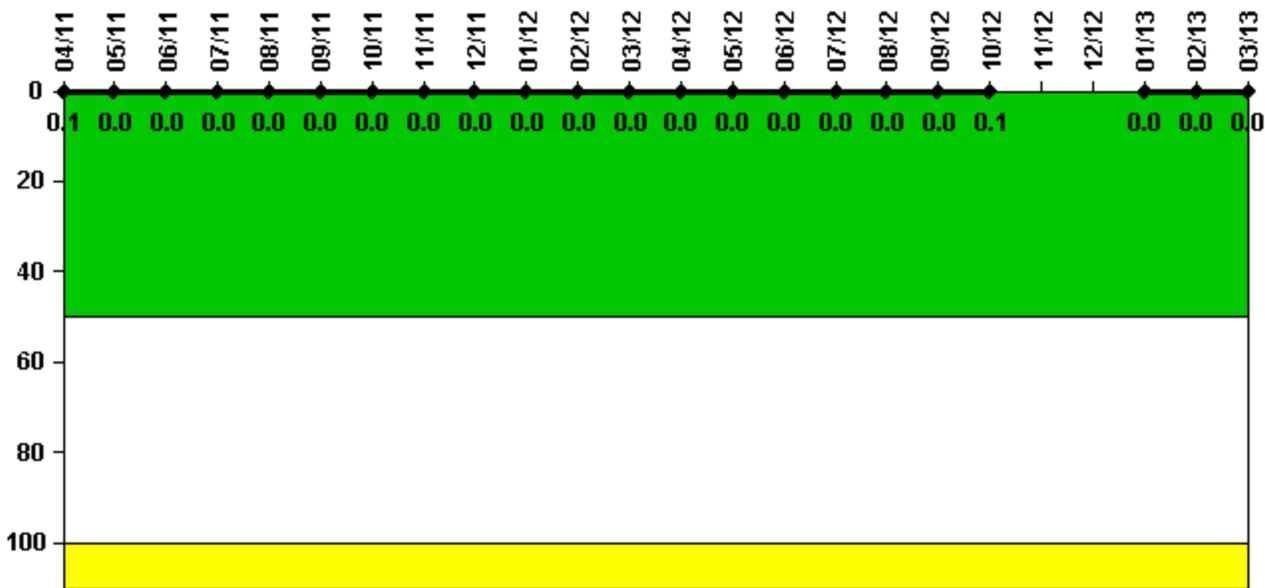

Thresholds: White > 50.0 Yellow > 100.0


Notes

Reactor Coolant System Activity	4/11	5/11	6/11	7/11	8/11	9/11	10/11	11/11	12/11	1/12	2/12	3/12
Maximum activity	0.000355	0.000133	0.000111	0.000090	0.000098	0.000091	0.000077	0.000089	0.000101	0.000117	0.000124	0.000122
Technical specification limit	0.4	0.4	0.4	0.4	0.4	0.4	0.4	0.4	0.4	0.4	0.4	0.4
Indicator value	0.1	0	0	0	0	0	0	0	0	0	0	0

Reactor Coolant System Activity	4/12	5/12	6/12	7/12	8/12	9/12	10/12	11/12	12/12	1/13	2/13	3/13
Maximum activity	0.000139	0.000144	0.000156	0.000155	0.000154	0.000139	0.000178	N/A	N/A	0.000056	0.000070	0.000081
Technical specification limit	0.4	0.4	0.4	0.4	0.4	0.4	0.4	0.4	0.4	0.4	0.4	0.4
Indicator value	0	0	0	0	0	0	0.1	N/A	N/A	0	0	0

Licensee Comments: none

Reactor Coolant System Leakage

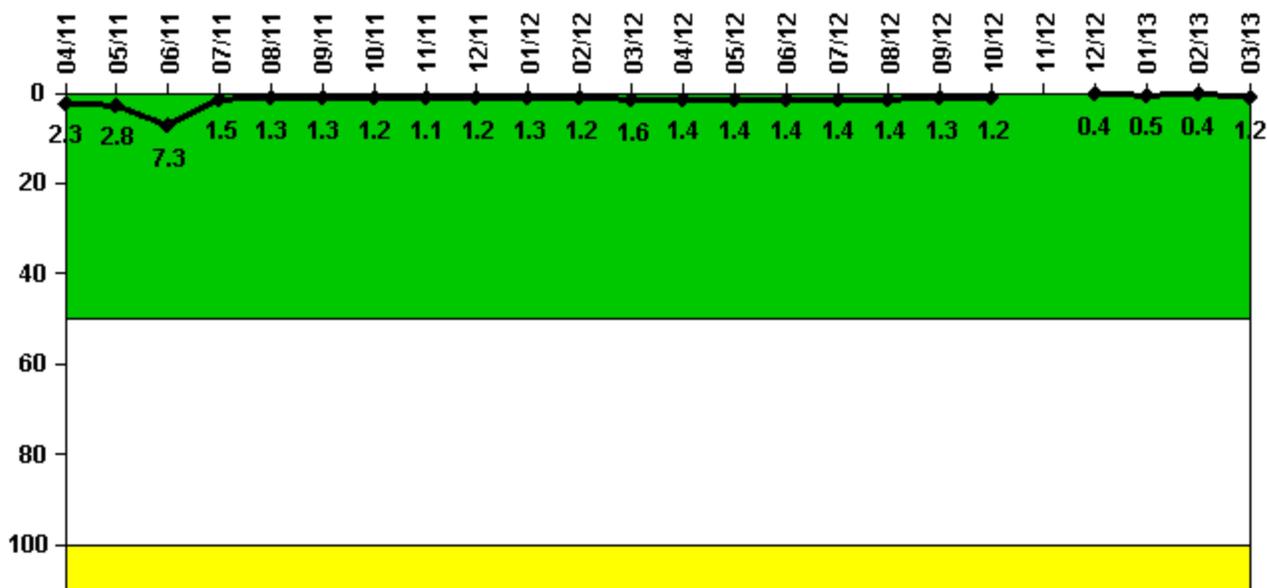


Thresholds: White > 50.0 Yellow > 100.0

Notes

Reactor Coolant System Leakage	4/11	5/11	6/11	7/11	8/11	9/11	10/11	11/11	12/11	1/12	2/12	3/12
Maximum leakage	0.230	0.280	0.730	0.150	0.130	0.130	0.120	0.110	0.120	0.130	0.120	0.160
Technical specification limit	10.0	10.0	10.0	10.0	10.0	10.0	10.0	10.0	10.0	10.0	10.0	10.0
Indicator value	2.3	2.8	7.3	1.5	1.3	1.3	1.2	1.1	1.2	1.3	1.2	1.6
Reactor Coolant System Leakage	4/12	5/12	6/12	7/12	8/12	9/12	10/12	11/12	12/12	1/13	2/13	3/13
Maximum leakage	0.140	0.140	0.140	0.140	0.140	0.130	0.120	N/A	0.040	0.050	0.040	0.120
Technical specification limit	10.0	10.0	10.0	10.0	10.0	10.0	10.0	10.0	10.0	10.0	10.0	10.0
Indicator value	1.4	1.4	1.4	1.4	1.4	1.3	1.2	N/A	0.4	0.5	0.4	1.2

Licensee Comments: none

Drill/Exercise Performance

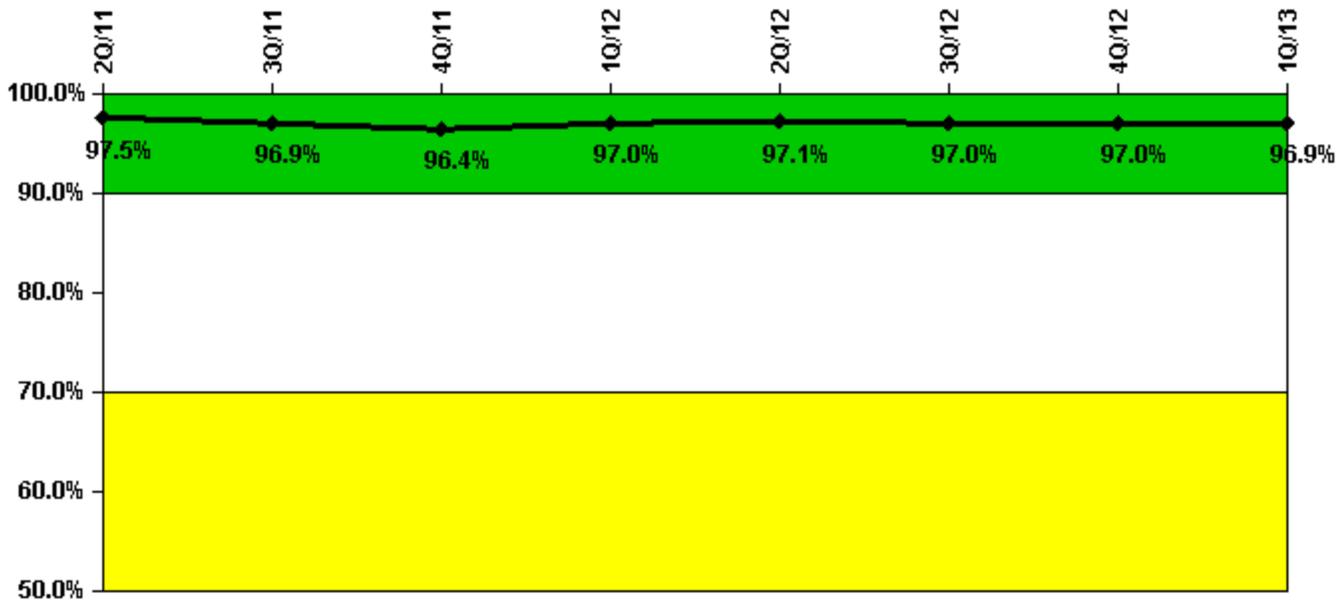


Thresholds: White < 90.0% Yellow < 70.0%

Notes

Drill/Exercise Performance	2Q/11	3Q/11	4Q/11	1Q/12	2Q/12	3Q/12	4Q/12	1Q/13
Successful opportunities	4.0	34.0	70.0	6.0	32.0	87.0	10.0	41.0
Total opportunities	4.0	36.0	73.0	6.0	32.0	90.0	10.0	42.0
Indicator value	97.5%	96.9%	96.4%	97.0%	97.1%	97.0%	97.0%	96.9%

Licensee Comments: none

ERO Drill Participation

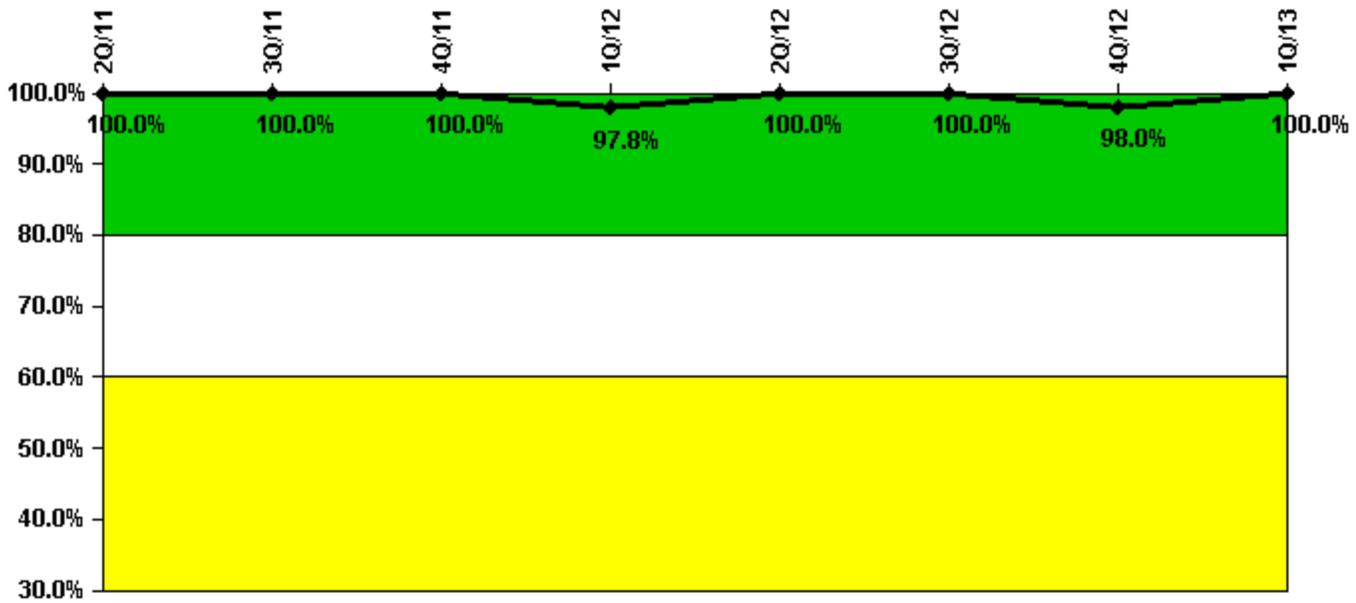


Thresholds: White < 80.0% Yellow < 60.0%

Notes

ERO Drill Participation	2Q/11	3Q/11	4Q/11	1Q/12	2Q/12	3Q/12	4Q/12	1Q/13
Participating Key personnel	75.0	74.0	90.0	88.0	99.0	97.0	99.0	97.0
Total Key personnel	75.0	74.0	90.0	90.0	99.0	97.0	101.0	97.0
Indicator value	100.0%	100.0%	100.0%	97.8%	100.0%	100.0%	98.0%	100.0%

Licensee Comments: none

Alert & Notification System

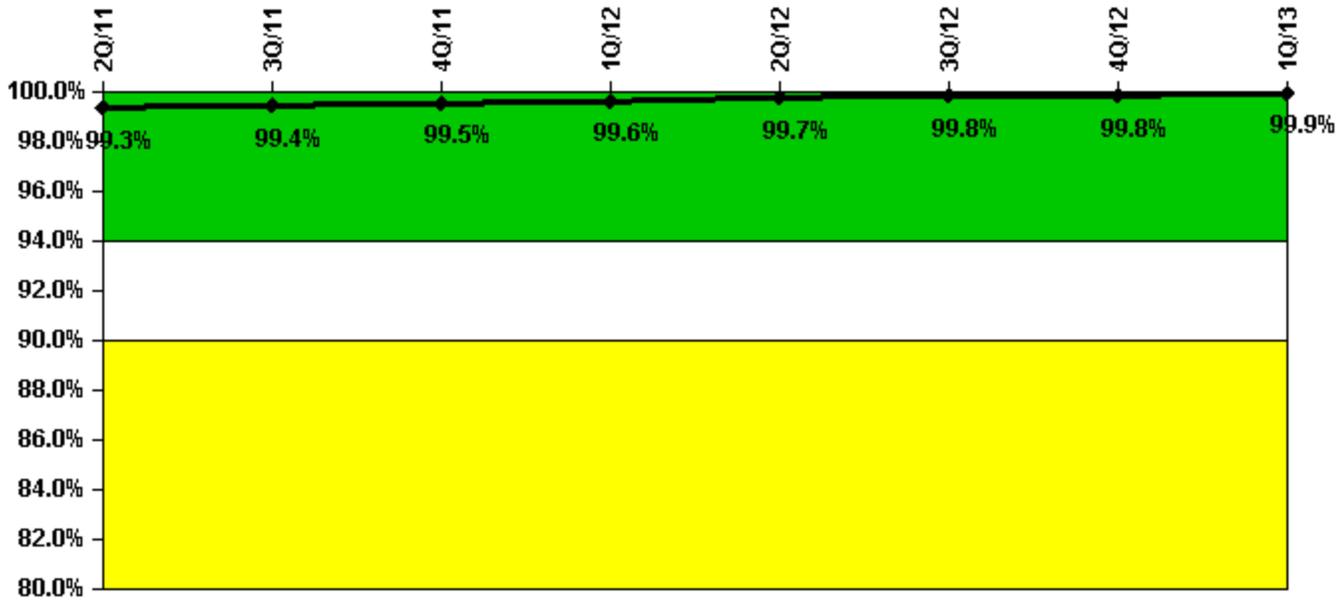


Thresholds: White < 94.0% Yellow < 90.0%

Notes

Alert & Notification System	2Q/11	3Q/11	4Q/11	1Q/12	2Q/12	3Q/12	4Q/12	1Q/13
Successful siren-tests	967	857	862	863	864	861	753	978
Total sirens-tests	972	864	864	864	864	864	755	978
Indicator value	99.3%	99.4%	99.5%	99.6%	99.7%	99.8%	99.8%	99.9%

Licensee Comments: none

Occupational Exposure Control Effectiveness

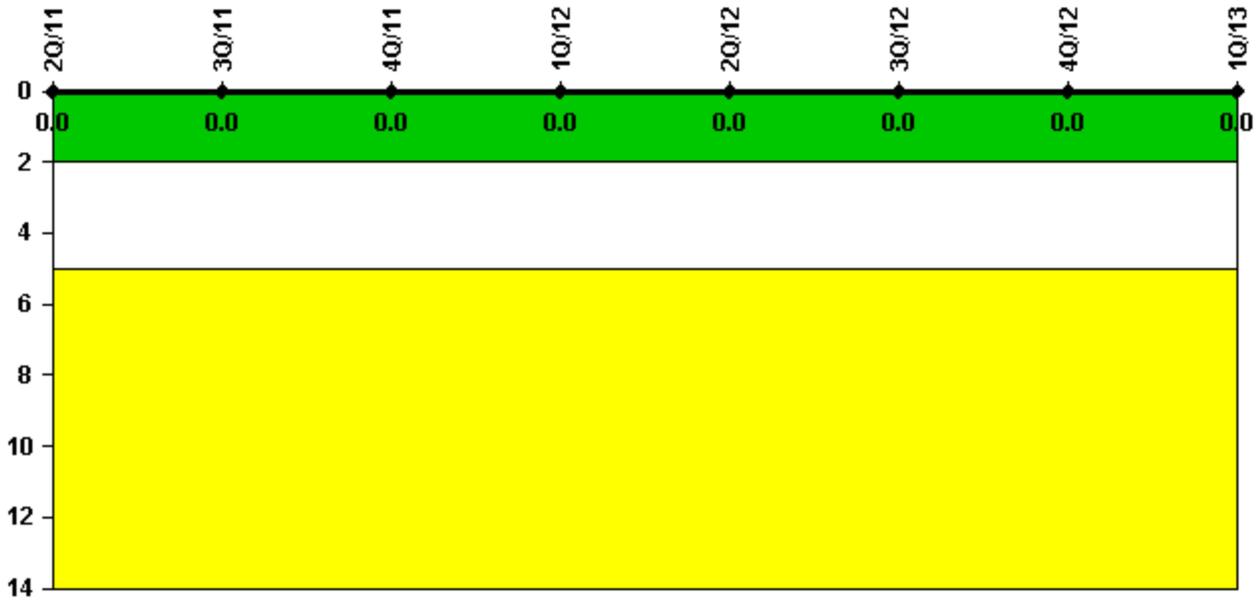


Thresholds: White > 2.0 Yellow > 5.0

Notes

Occupational Exposure Control Effectiveness	2Q/11	3Q/11	4Q/11	1Q/12	2Q/12	3Q/12	4Q/12	1Q/13
High radiation area occurrences	0	0	0	0	0	0	0	0
Very high radiation area occurrences	0	0	0	0	0	0	0	0
Unintended exposure occurrences	0	0	0	0	0	0	0	0
Indicator value	0							

Licensee Comments: none

RETS/ODCM Radiological Effluent

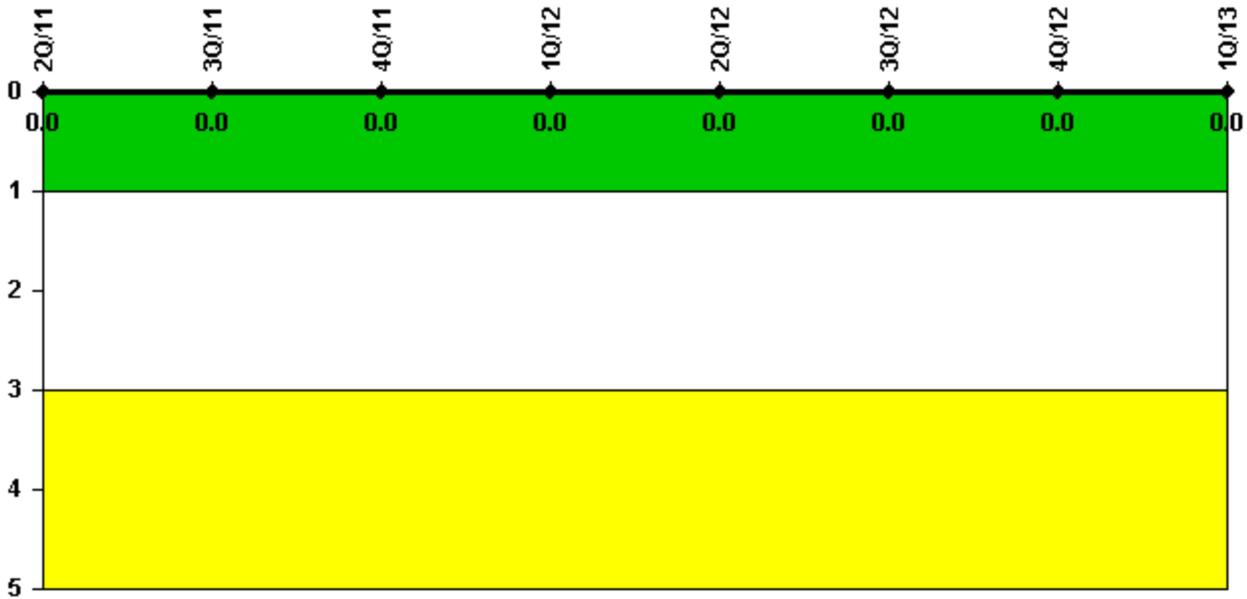

Thresholds: White > 1.0 Yellow > 3.0

Notes

RETS/ODCM Radiological Effluent	2Q/11	3Q/11	4Q/11	1Q/12	2Q/12	3Q/12	4Q/12	1Q/13
RETS/ODCM occurrences	0	0	0	0	0	0	0	0
Indicator value	0							

Licensee Comments: none

Although the Security Cornerstone is included in the Reactor Oversight Process assessment program, the Commission has decided that specific information related to findings and performance indicators pertaining to the Security Cornerstone will not be publicly available to ensure that security information is not provided to a possible adversary. Other than the fact that a finding or performance indicator is Green or Greater-Than-Green, security related information will not be displayed on the public web page.

 [Action Matrix Summary](#) | [Inspection Findings Summary](#) | [PI Summary](#) | [Reactor Oversight Process](#)

Last Modified: April 23, 2013
