


Monticello

2Q/2014 Performance Indicators

The solid trend line represents the current reporting period.

Licensee's General Comments: none

Unplanned Scrams per 7000 Critical Hrs

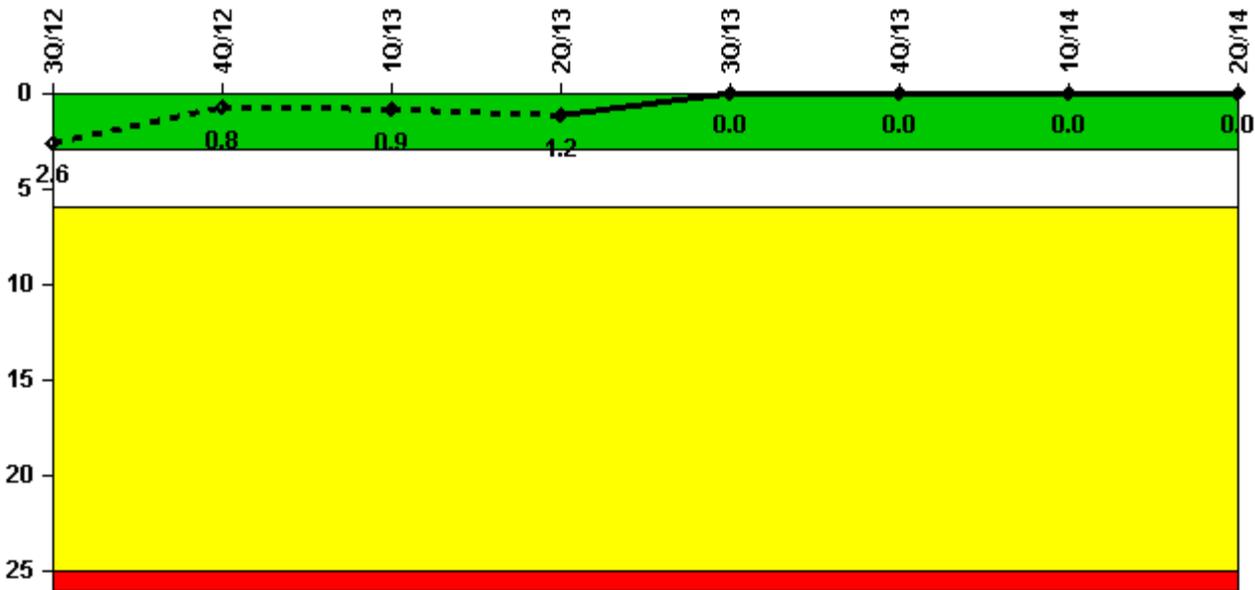


Thresholds: White > 3.0 Yellow > 6.0 Red > 25.0

Notes

Unplanned Scrams per 7000 Critical Hrs	3Q/12	4Q/12	1Q/13	2Q/13	3Q/13	4Q/13	1Q/14	2Q/14
Unplanned scrams	1.0	0	0	0	0	0	0	0
Critical hours	2082.0	2209.0	1442.6	0	1826.8	2209.0	1722.5	2184.0
Indicator value	2.6	0.8	0.9	1.2	0	0	0	0

Licensee Comments: none

Unplanned Power Changes per 7000 Critical Hrs

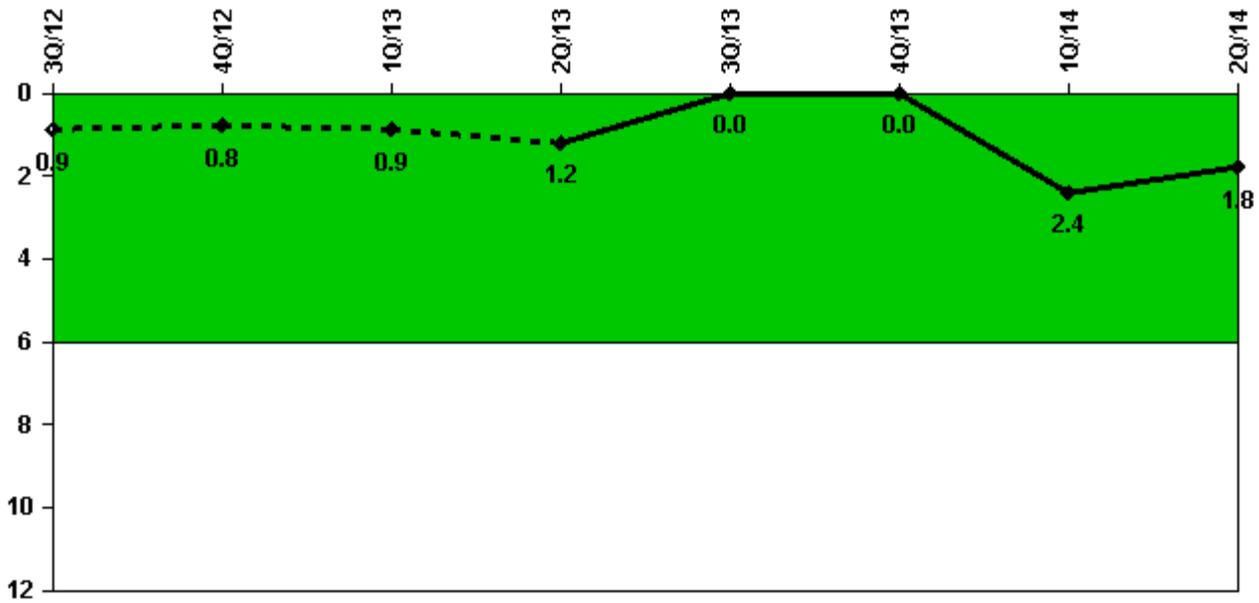


Thresholds: White > 6.0

Notes

Unplanned Power Changes per 7000 Critical Hrs	3Q/12	4Q/12	1Q/13	2Q/13	3Q/13	4Q/13	1Q/14	2Q/14
Unplanned power changes	1.0	0	0	0	0	0	2.0	0
Critical hours	2082.0	2209.0	1442.6	0	1826.8	2209.0	1722.5	2184.0
Indicator value	0.9	0.8	0.9	1.2	0	0	2.4	1.8

Licensee Comments: none

Unplanned Scrams with Complications

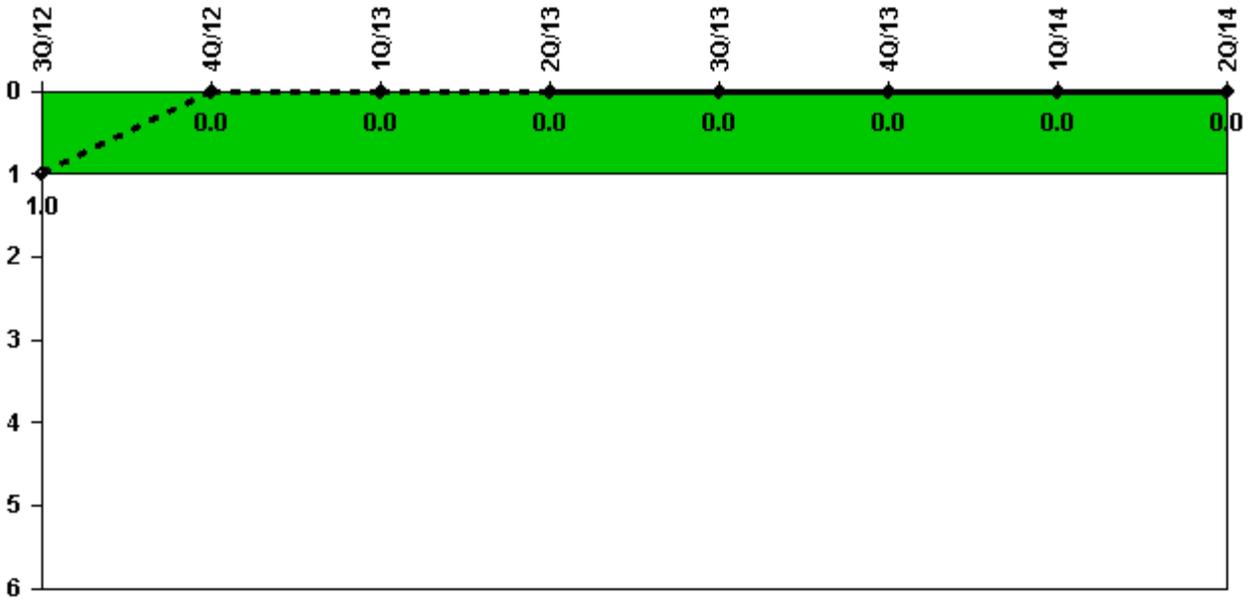


Thresholds: White > 1.0

Notes

Unplanned Scrams with Complications	3Q/12	4Q/12	1Q/13	2Q/13	3Q/13	4Q/13	1Q/14	2Q/14
Scrams with complications	0	0	0	0	0	0	0	0
Indicator value	1.0	0.0						

Licensee Comments: none

Safety System Functional Failures (BWR)

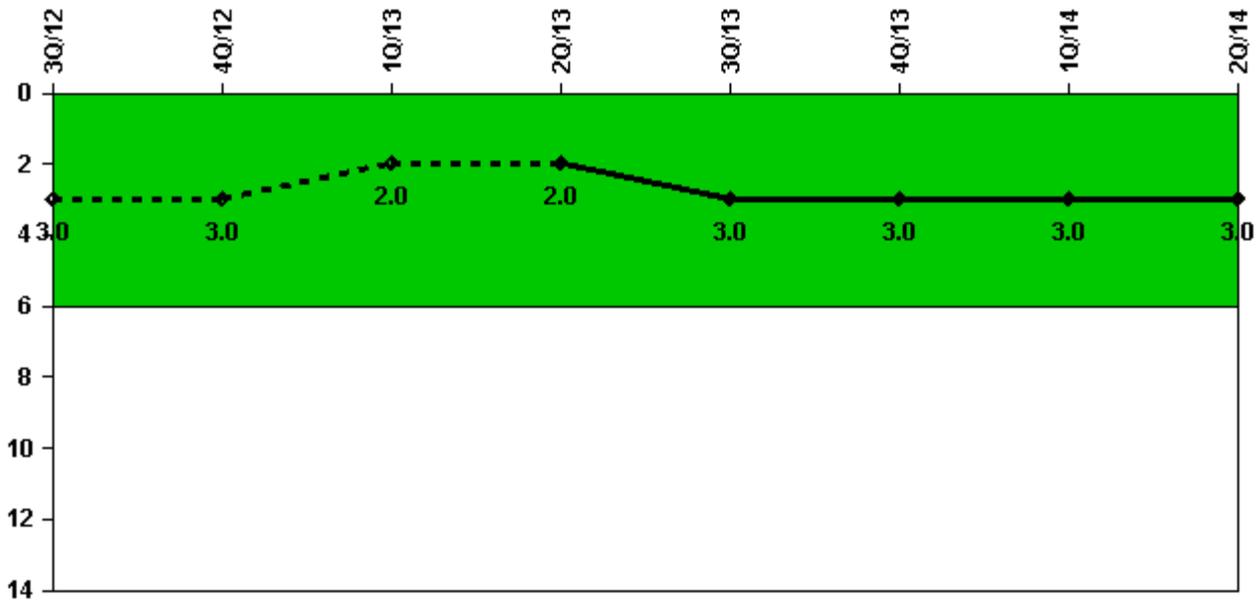

Thresholds: White > 6.0

Notes

Safety System Functional Failures (BWR)	3Q/12	4Q/12	1Q/13	2Q/13	3Q/13	4Q/13	1Q/14	2Q/14
Safety System Functional Failures	1	1	0	0	2	1	0	0
Indicator value	3	3	2	2	3	3	3	3

Licensee Comments:

1Q/14: The indicator value for the 4Q2013 was revised to remove one SSFF (LER 2013-008) based on engineering analysis. The change did not affect the color of the indicator.

4Q/13: LER 2013-008, LER 2013-006


4Q/13: LER 2013-008, LER 2013-006 The indicator value for the 4Q2013 was revised to remove one SSFF (LER 2013-008) based on engineering analysis. The change did not affect the color of the indicator.

3Q/13: LER 2013-003-01, LER 2013-004

4Q/12: LER 2012-004

3Q/12: LER 2012-001, 7/5/2012

Mitigating Systems Performance Index, Emergency AC Power System

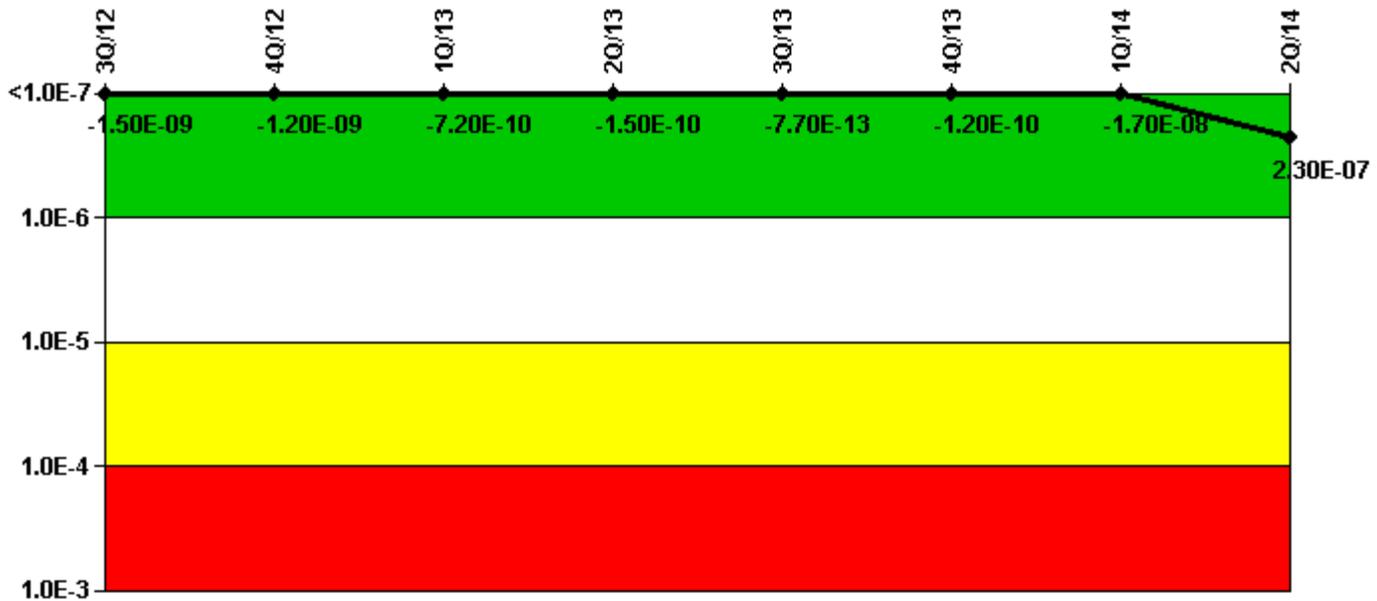

Thresholds: White > 1.00E-6 Yellow > 1.00E-5 Red > 1.00E-4

Notes


Mitigating Systems Performance Index, Emergency AC Power System	3Q/12	4Q/12	1Q/13	2Q/13	3Q/13	4Q/13	1Q/14	2Q/14
UAI (Δ CDF)	-7.80E-10	-8.43E-10	-7.23E-10	-3.42E-10	-6.03E-10	-1.15E-09	-1.79E-08	-6.59E-09
URI (Δ CDF)	-7.43E-10	-3.77E-10	2.50E-12	1.94E-10	6.02E-10	1.03E-09	7.65E-10	2.36E-07
PLE	NO							
Indicator value	-1.50E-09	-1.20E-09	-7.20E-10	-1.50E-10	-7.70E-13	-1.20E-10	-1.70E-08	2.30E-07

Licensee Comments:

2Q/14: Changed PRA Parameter(s). Revision to estimated test demands and run hours due to identification of a change > 25%, per NEI 99-02. Revision 3.2 of the Monticello PRA Level 1 Quantification Notebook (PRA-MT-QU) was approved March 31st, 2014 with a corresponding MSPI Basis document Revision 5 approved 7/09/2014. The Rev 3.2 PRA model incorporated the modification/procedure changes required to pin the condensate demineralizer AOVs. As a result of the PRA model change, the CDF, Fussell-Vesely and Basic Event Probabilities for all monitored trains and components were revised.

1Q/14: Changed PRA Parameter(s). The Monticello Revision 3.1 model was approved October 1st, 2013 with a corresponding MSPI Basis document Revision 4 approved 4/18/2014. The PRA model revision was created to meet the RG 1.200, Rev 2 Standard. As a result of the PRA model change, the CDF, Fussell-Vesely and Basic Event Probabilities for all monitored trains and components were revised.

Mitigating Systems Performance Index, High Pressure Injection System

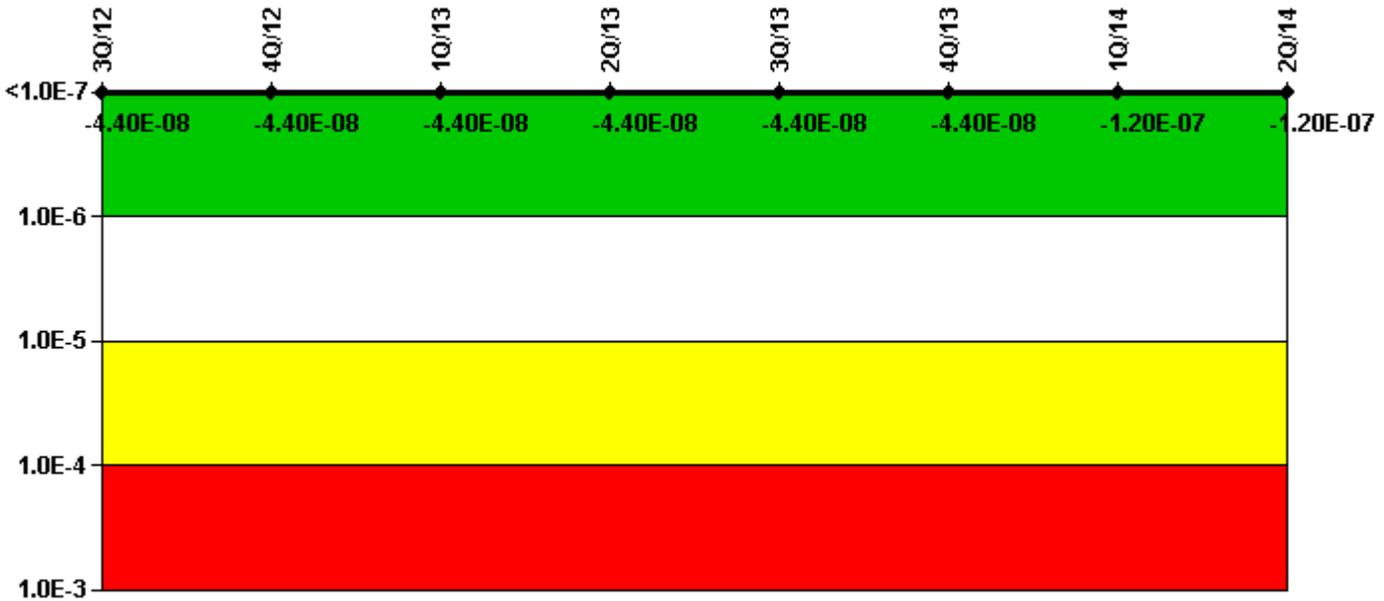

Thresholds: White > 1.00E-6 Yellow > 1.00E-5 Red > 1.00E-4

Notes


Mitigating Systems Performance Index, High Pressure Injection System	3Q/12	4Q/12	1Q/13	2Q/13	3Q/13	4Q/13	1Q/14	2Q/14
UAI (Δ CDF)	-1.68E-08	-1.68E-08	-1.68E-08	-1.68E-08	-1.68E-08	-1.68E-08	-4.33E-08	-4.33E-08
URI (Δ CDF)	-2.71E-08	-2.71E-08	-2.71E-08	-2.71E-08	-2.71E-08	-2.71E-08	-7.21E-08	-7.32E-08
PLE	NO							
Indicator value	-4.40E-08	-4.40E-08	-4.40E-08	-4.40E-08	-4.40E-08	-4.40E-08	-1.20E-07	-1.20E-07

Licensee Comments:

2Q/14: Changed PRA Parameter(s). Revision to estimated test demands and run hours due to identification of a change > 25%, per NEI 99-02. Revision 3.2 of the Monticello PRA Level 1 Quantification Notebook (PRA-MT-QU) was approved March 31st, 2014 with a corresponding MSPI Basis document Revision 5 approved 7/09/2014. The Rev 3.2 PRA model incorporated the modification/procedure changes required to pin the condensate demineralizer AOVs. As a result of the PRA model change, the CDF, Fussell-Vesely and Basic Event Probabilities for all monitored trains and components were revised.

1Q/14: Changed PRA Parameter(s). The Monticello Revision 3.1 model was approved October 1st, 2013 with a corresponding MSPI Basis document Revision 4 approved 4/18/2014. The PRA model revision was created to meet the RG 1.200, Rev 2 Standard. As a result of the PRA model change, the CDF, Fussell-Vesely and Basic Event Probabilities for all monitored trains and components were revised.

Mitigating Systems Performance Index, Heat Removal System

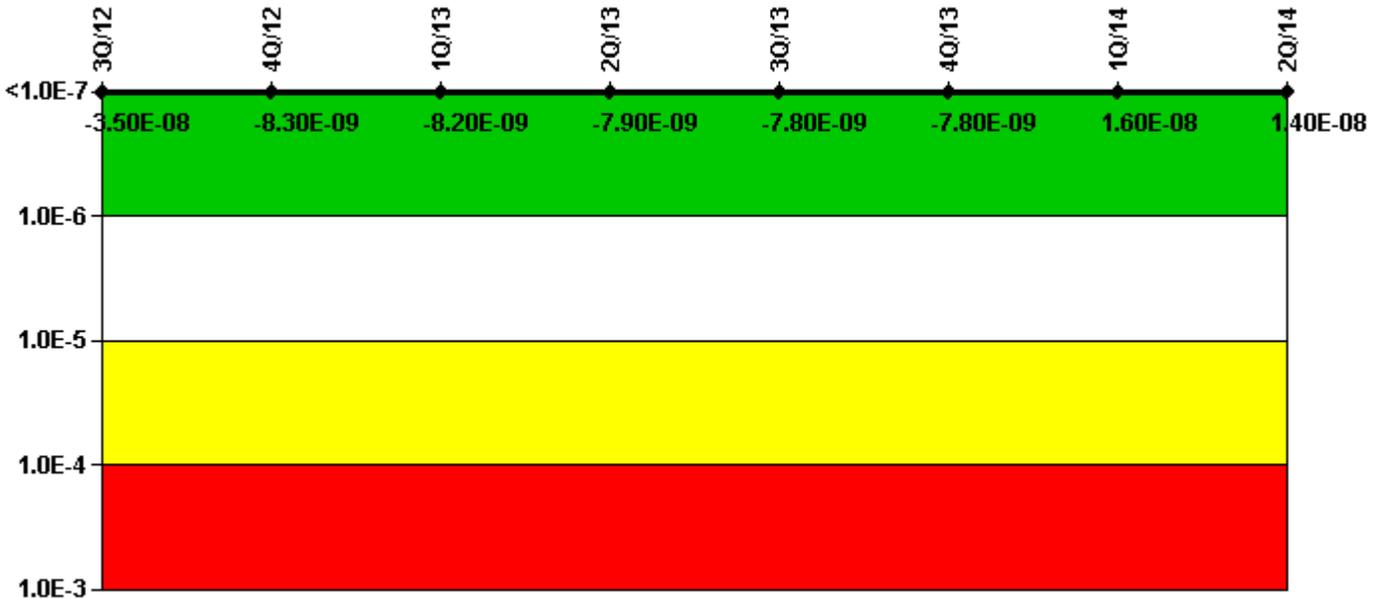

Thresholds: White > 1.00E-6 Yellow > 1.00E-5 Red > 1.00E-4

Notes

Mitigating Systems Performance Index, Heat Removal System	3Q/12	4Q/12	1Q/13	2Q/13	3Q/13	4Q/13	1Q/14	2Q/14
UAI (Δ CDF)	-1.44E-08	-1.15E-08	-1.14E-08	-1.11E-08	-1.10E-08	-1.10E-08	-2.67E-08	-2.73E-08
URI (Δ CDF)	-2.11E-08	3.18E-09	3.18E-09	3.18E-09	3.18E-09	3.18E-09	4.25E-08	4.12E-08
PLE	NO							
Indicator value	-3.50E-08	-8.30E-09	-8.20E-09	-7.90E-09	-7.80E-09	-7.80E-09	1.60E-08	1.40E-08


Licensee Comments:

2Q/14: Changed PRA Parameter(s). Revision to estimated test demands and run hours due to identification of a change > 25%, per NEI 99-02. Revision 3.2 of the Monticello PRA Level 1 Quantification Notebook (PRA-MT-QU) was approved March 31st, 2014 with a corresponding MSPI Basis document Revision 5 approved 7/09/2014. The Rev 3.2 PRA model incorporated the modification/procedure changes required to pin the condensate demineralizer AOVs. As a result of the PRA model change, the CDF, Fussell-Vesely and Basic Event Probabilities for all monitored trains and components were revised.

1Q/14: Changed PRA Parameter(s). The Monticello Revision 3.1 model was approved October 1st, 2013 with a corresponding MSPI Basis document Revision 4 approved 4/18/2014. The PRA model revision was created to meet the RG 1.200, Rev 2 Standard. As a result of the PRA model change, the CDF, Fussell-Vesely and Basic

Event Probabilities for all monitored trains and components were revised.

Mitigating Systems Performance Index, Residual Heat Removal System

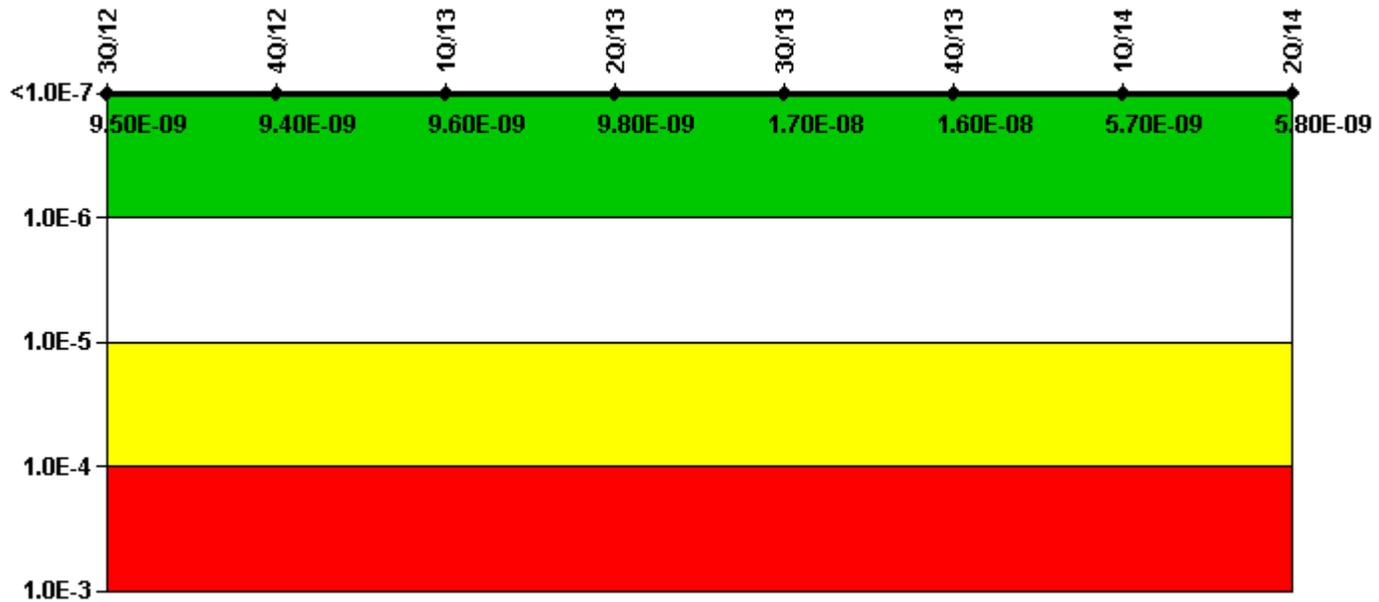

Thresholds: White > 1.00E-6 Yellow > 1.00E-5 Red > 1.00E-4

Notes

Mitigating Systems Performance Index, Residual Heat Removal System	3Q/12	4Q/12	1Q/13	2Q/13	3Q/13	4Q/13	1Q/14	2Q/14
UAI (Δ CDF)	-2.23E-10	-2.73E-10	-3.05E-11	8.66E-11	1.95E-10	-3.83E-10	-3.62E-10	-3.58E-10
URI (Δ CDF)	9.68E-09	9.68E-09	9.68E-09	9.68E-09	1.67E-08	1.67E-08	6.06E-09	6.16E-09
PLE	NO							
Indicator value	9.50E-09	9.40E-09	9.60E-09	9.80E-09	1.70E-08	1.60E-08	5.70E-09	5.80E-09


Licensee Comments:

2Q/14: Changed PRA Parameter(s). Revision 3.2 of the Monticello PRA Level 1 Quantification Notebook (PRA-MT-QU) was approved March 31st, 2014 with a corresponding MSPI Basis document Revision 5 approved 7/09/2014. The Rev 3.2 PRA model incorporated the modification/procedure changes required to pin the condensate demineralizer AOVs. As a result of the PRA model change, the CDF, Fussel-Vesely and Basic Event Probabilities for all monitored trains and components were revised.

1Q/14: Changed PRA Parameter(s). The Monticello Revision 3.1 model was approved October 1st, 2013 with a

corresponding MSPI Basis document Revision 4 approved 4/18/2014. The PRA model revision was created to meet the RG 1.200, Rev 2 Standard. As a result of the PRA model change, the CDF, Fussell-Vesely and Basic Event Probabilities for all monitored trains and components were revised.

Mitigating Systems Performance Index, Cooling Water Systems

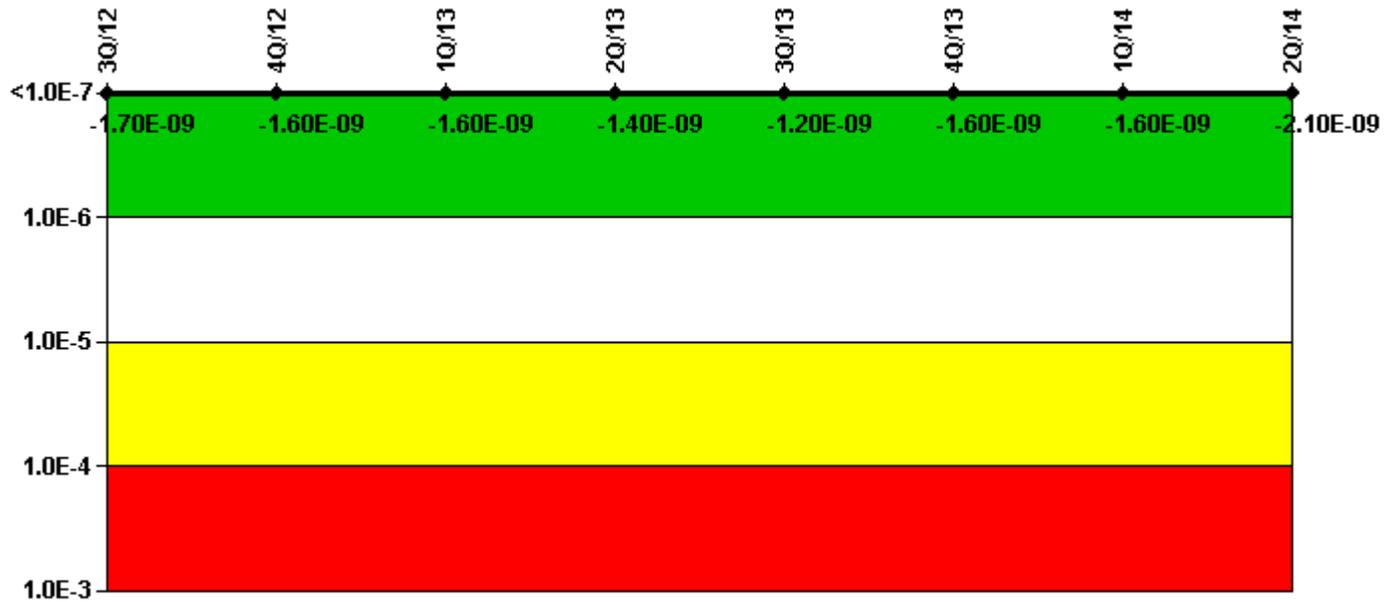

Thresholds: White > 1.00E-6 Yellow > 1.00E-5 Red > 1.00E-4

Notes

Mitigating Systems Performance Index, Cooling Water Systems	3Q/12	4Q/12	1Q/13	2Q/13	3Q/13	4Q/13	1Q/14	2Q/14
UAI (ΔCDF)	-1.66E-09	-1.57E-09	-1.59E-09	-1.37E-09	-1.21E-09	-1.64E-09	-1.68E-09	-2.19E-09
URI (ΔCDF)	2.55E-12	2.55E-12	2.55E-12	2.55E-12	2.55E-12	1.75E-11	5.04E-11	3.89E-11
PLE	NO							
Indicator value	-1.70E-09	-1.60E-09	-1.60E-09	-1.40E-09	-1.20E-09	-1.60E-09	-1.60E-09	-2.10E-09


Licensee Comments:

2Q/14: Changed PRA Parameter(s). Revision 3.2 of the Monticello PRA Level 1 Quantification Notebook (PRA-MT-QU) was approved March 31st, 2014 with a corresponding MSPI Basis document Revision 5 approved 7/09/2014. The Rev 3.2 PRA model incorporated the modification/procedure changes required to pin the condensate demineralizer AOVs. As a result of the PRA model change, the CDF, Fussell-Vesely and Basic Event Probabilities for all monitored trains and components were revised.

1Q/14: Changed PRA Parameter(s). The Monticello Revision 3.1 model was approved October 1st, 2013 with a corresponding MSPI Basis document Revision 4 approved 4/18/2014. The PRA model revision was created to meet the RG 1.200, Rev 2 Standard. As a result of the PRA model change, the CDF, Fussell-Vesely and Basic Event Probabilities for all monitored trains and components were revised.

4Q/13: Final engineering evaluation of Dec 2013 determined MSPI failure in cooling water system. Change did not result in a color change of the indicator.

Reactor Coolant System Activity

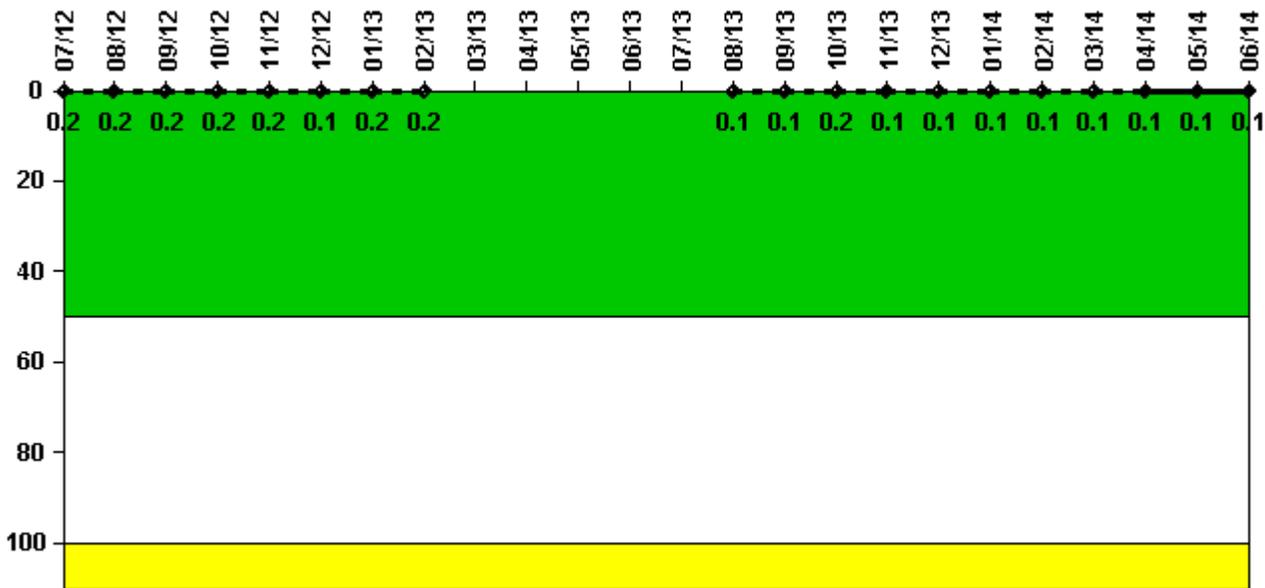

Thresholds: White > 50.0 Yellow > 100.0

Notes

Reactor Coolant System Activity		7/12	8/12	9/12	10/12	11/12	12/12	1/13	2/13	3/13	4/13	5/13	6/13
Maximum activity		0.000344	0.000399	0.000420	0.000354	0.000316	0.000273	0.000343	0.000302	N/A	N/A	N/A	N/A
Technical specification limit		0.2	0.2	0.2	0.2	0.2	0.2	0.2	0.2	0.2	0.2	0.2	0.2
Indicator value		0.2	0.2	0.2	0.2	0.2	0.1	0.2	0.2	N/A	N/A	N/A	N/A
Reactor Coolant System Activity		7/13	8/13	9/13	10/13	11/13	12/13	1/14	2/14	3/14	4/14	5/14	6/14
Maximum activity		N/A	0.000232	0.000248	0.000339	0.000174	0.000166	0.000129	0.000252	0.000190	0.000160	0.000114	0.000131
Technical specification limit		0.2	0.2	0.2	0.2	0.2	0.2	0.2	0.2	0.2	0.2	0.2	0.2

Indicator value	N/A	0.1	0.1	0.2	0.1	0.1	0.1	0.1	0.1	0.1	0.1	0.1	0.1
-----------------	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----


Licensee Comments:

9/13: Plant conditions were not met to calculate RCS activity for July 2013.

6/13: Plant Conditions do not require RCS activity to be calculated for April, May and June 2013.

3/13: Plant conditions were not met to calculate RCS activity for March 2013.

Reactor Coolant System Leakage

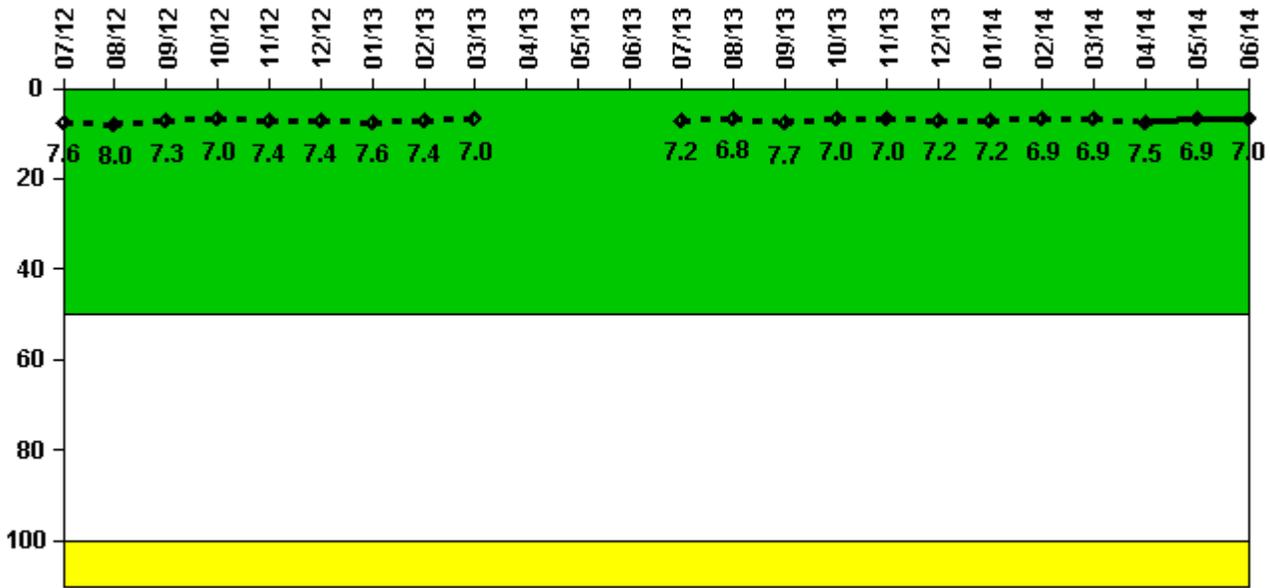

Thresholds: White > 50.0 Yellow > 100.0

Notes

Reactor Coolant System Leakage	7/12	8/12	9/12	10/12	11/12	12/12	1/13	2/13	3/13	4/13	5/13	6/13
Maximum leakage	1.900	2.000	1.820	1.750	1.840	1.840	1.900	1.840	1.760	N/A	N/A	N/A
Technical specification limit	25.0	25.0	25.0	25.0	25.0	25.0	25.0	25.0	25.0	25.0	25.0	25.0
Indicator value	7.6	8.0	7.3	7.0	7.4	7.4	7.6	7.4	7.0	N/A	N/A	N/A
Reactor Coolant System Leakage	7/13	8/13	9/13	10/13	11/13	12/13	1/14	2/14	3/14	4/14	5/14	6/14
Maximum leakage	1.800	1.690	1.920	1.740	1.760	1.790	1.800	1.720	1.720	1.880	1.730	1.760
Technical specification limit	25.0	25.0	25.0	25.0	25.0	25.0	25.0	25.0	25.0	25.0	25.0	25.0


Indicator value	7.2	6.8	7.7	7.0	7.0	7.2	7.2	6.9	6.9	7.5	6.9	7.0
-----------------	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----

Licensee Comments:

6/13: Plant Conditions do not require RCS Leakage to be calculated for April 2013, May 2013 and June 2013.

6/13: Plant Conditions do not require RCS Leakage to be calculated for April 2013, May 2013 and June 2013.

Drill/Exercise Performance

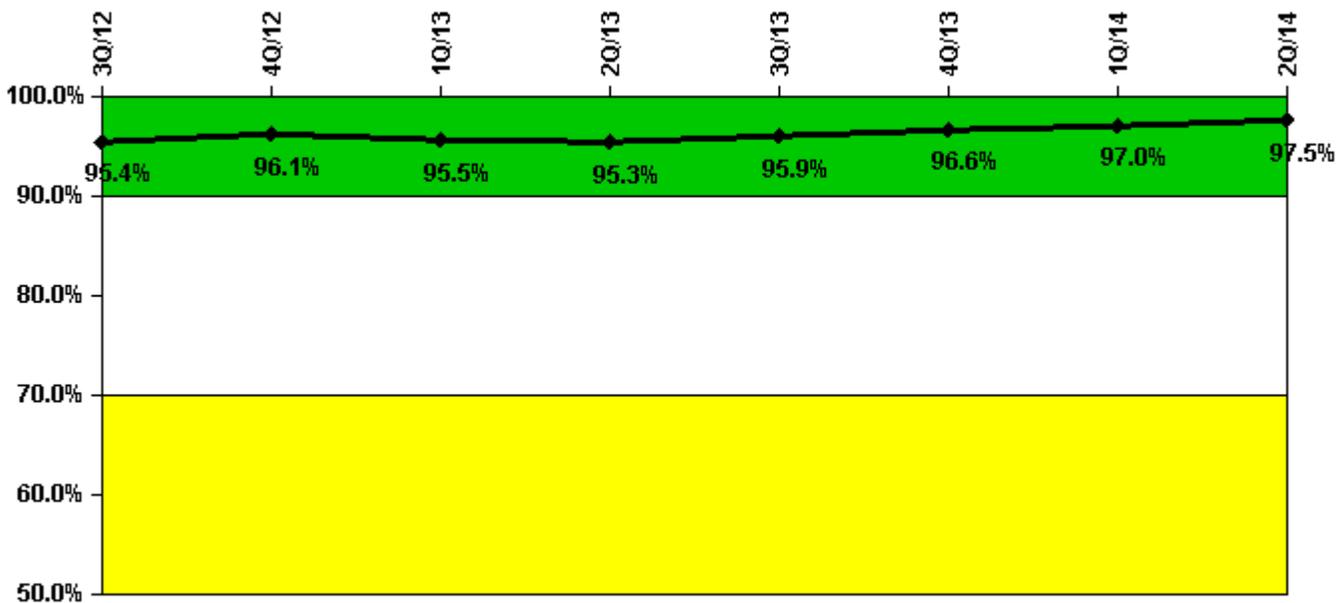

Thresholds: White < 90.0% Yellow < 70.0%


Notes

Drill/Exercise Performance	3Q/12	4Q/12	1Q/13	2Q/13	3Q/13	4Q/13	1Q/14	2Q/14
Successful opportunities	40.0	46.0	16.0	7.0	37.0	77.0	30.0	92.0
Total opportunities	42.0	46.0	19.0	7.0	39.0	79.0	30.0	92.0
Indicator value	95.4%	96.1%	95.5%	95.3%	95.9%	96.6%	97.0%	97.5%

Licensee Comments:

3Q/12: Sept 2012 ammended to include 6 successes for 6 opportunities due to licensed operator requail exam security that was unavaillable for 3rd quarter submittal. No color change.

ERO Drill Participation

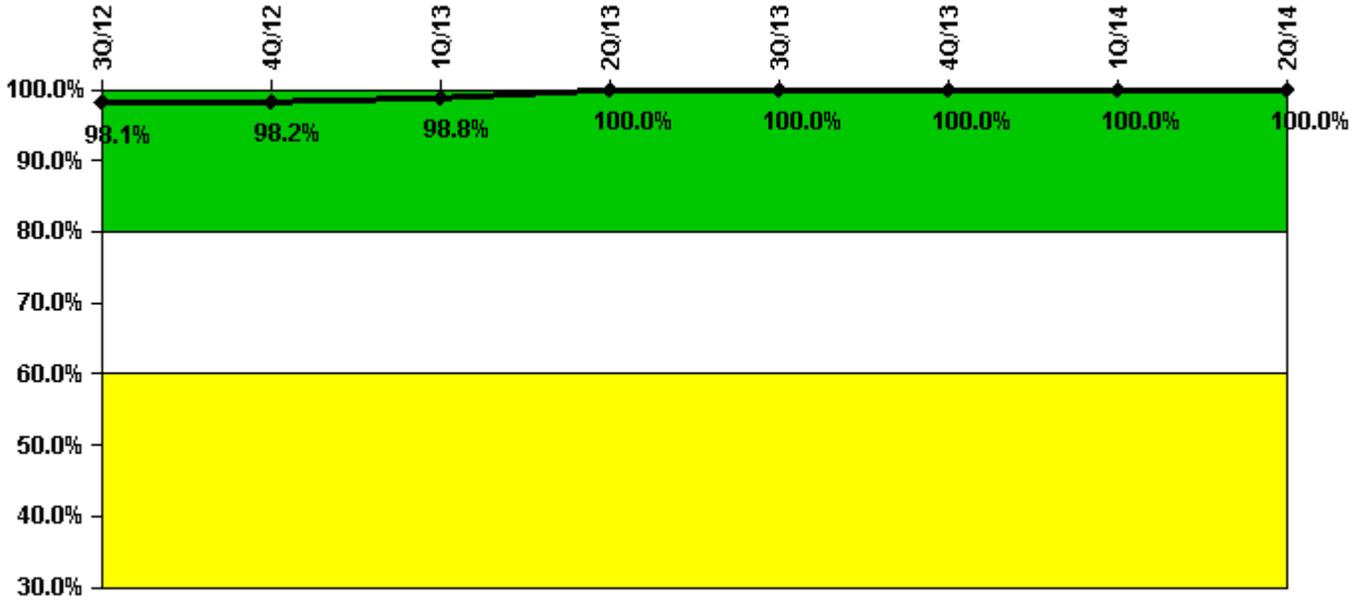


Thresholds: White < 80.0% Yellow < 60.0%

Notes

ERO Drill Participation	3Q/12	4Q/12	1Q/13	2Q/13	3Q/13	4Q/13	1Q/14	2Q/14
Participating Key personnel	151.0	163.0	160.0	173.0	165.0	164.0	155.0	154.0
Total Key personnel	154.0	166.0	162.0	173.0	165.0	164.0	155.0	154.0
Indicator value	98.1%	98.2%	98.8%	100.0%	100.0%	100.0%	100.0%	100.0%

Licensee Comments: none

Alert & Notification System

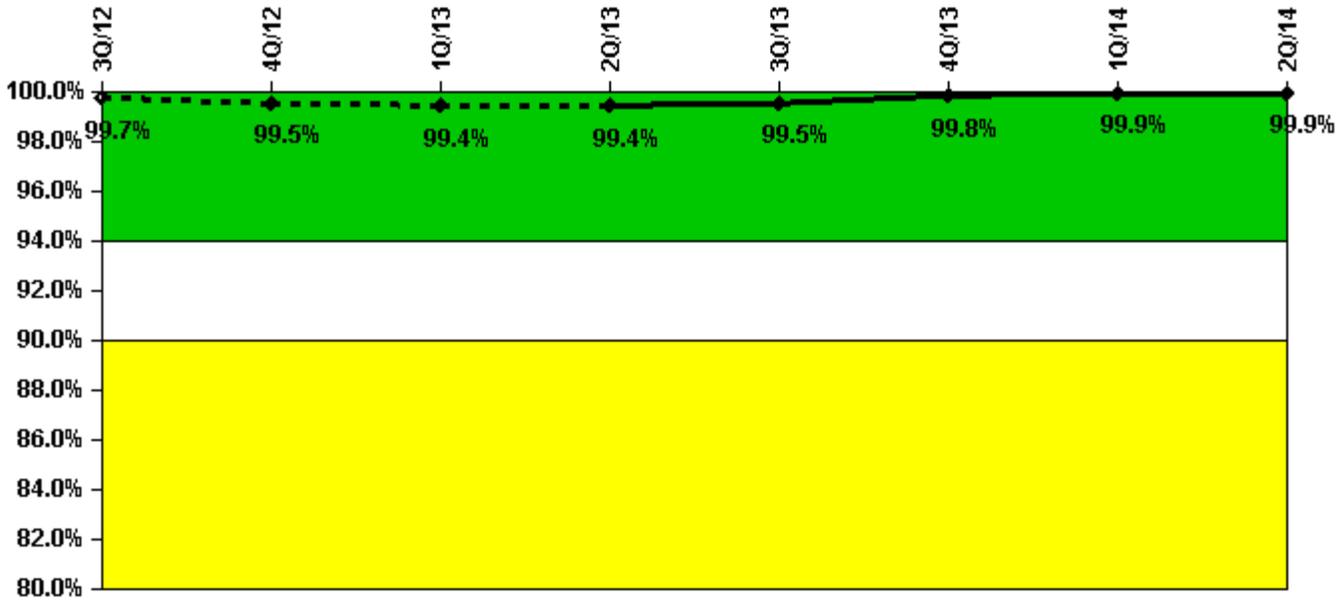

Thresholds: White < 94.0% Yellow < 90.0%

Notes


Alert & Notification System	3Q/12	4Q/12	1Q/13	2Q/13	3Q/13	4Q/13	1Q/14	2Q/14
Successful siren-tests	1374	1362	1368	1377	1377	1377	1376	1377
Total sirens-tests	1378	1378	1378	1378	1378	1378	1378	1378
Indicator value	99.7%	99.5%	99.4%	99.4%	99.5%	99.8%	99.9%	99.9%

Licensee Comments:

1Q/14: Alert and Notification System Reliability updated to reflect siren failure in July 2013. No color change.

3Q/13: Alert and Notification System Reliability updated to reflect siren failure in July 2013. No color change.

Occupational Exposure Control Effectiveness

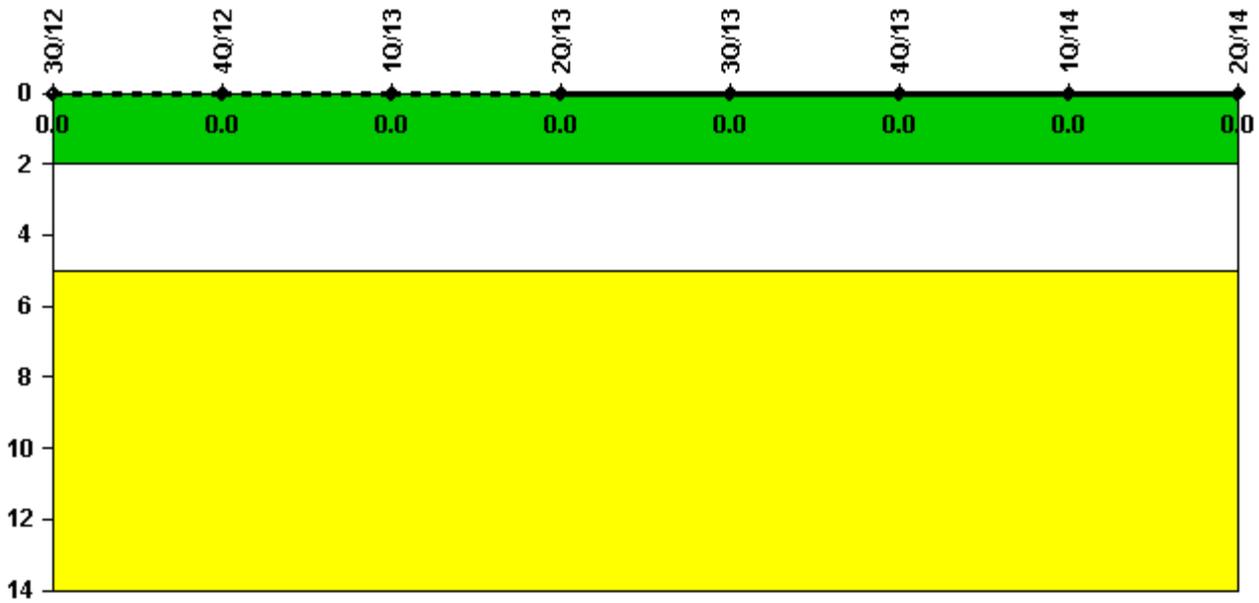


Thresholds: White > 2.0 Yellow > 5.0

Notes

Occupational Exposure Control Effectiveness	3Q/12	4Q/12	1Q/13	2Q/13	3Q/13	4Q/13	1Q/14	2Q/14
High radiation area occurrences	0	0	0	0	0	0	0	0
Very high radiation area occurrences	0	0	0	0	0	0	0	0
Unintended exposure occurrences	0	0	0	0	0	0	0	0
Indicator value	0							

Licensee Comments: none

RETS/ODCM Radiological Effluent

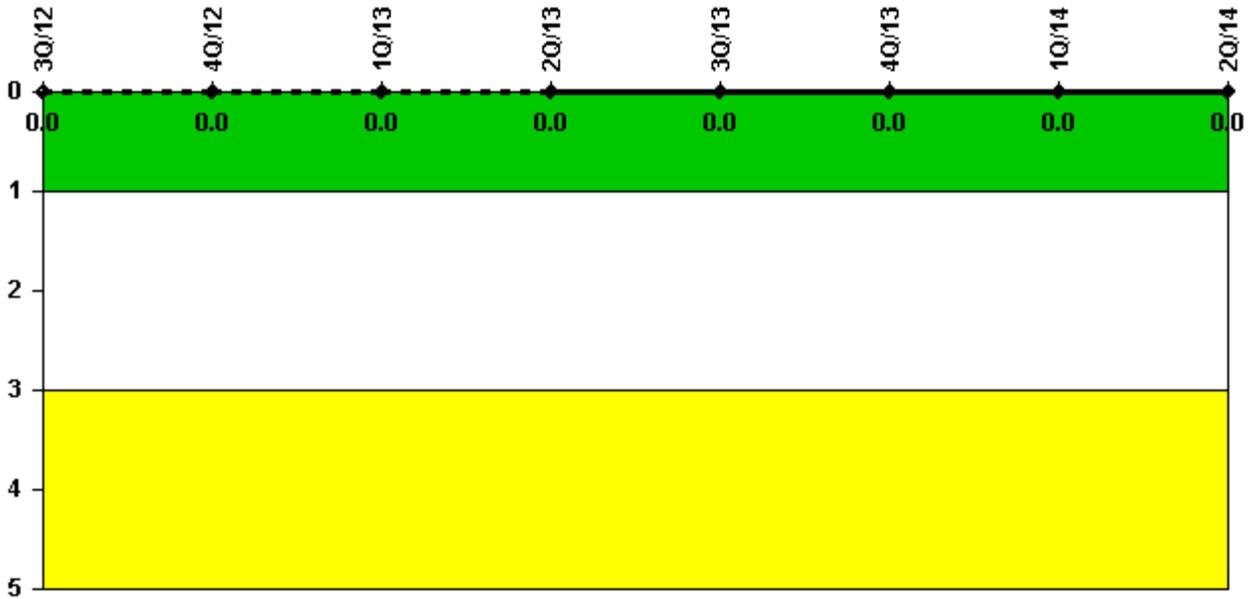

Thresholds: White > 1.0 Yellow > 3.0

Notes

RETS/ODCM Radiological Effluent	3Q/12	4Q/12	1Q/13	2Q/13	3Q/13	4Q/13	1Q/14	2Q/14
RETS/ODCM occurrences	0	0	0	0	0	0	0	0
Indicator value	0							

Licensee Comments: none

Although the Security Cornerstone is included in the Reactor Oversight Process assessment program, the Commission has decided that specific information related to findings and performance indicators pertaining to the Security Cornerstone will not be publicly available to ensure that security information is not provided to a possible adversary. Other than the fact that a finding or performance indicator is Green or Greater-Than-Green, security related information will not be displayed on the public web page.

 [Action Matrix Summary](#) | [Inspection Findings Summary](#) | [PI Summary](#) | [Reactor Oversight Process](#)

Last Modified: July 31, 2014
